6-7-71 V

bor. M.D.M.

#1

NE cor. sec. 2

T 41N. R 1W.

V 10-27-72

6-7-71 V

#1


NE cor. sec. 2

T 11 N., R 1 W

V 10-27-72

A limestone rock 36 x 12 x 6 ins. firmly set and dimly marked, on steel post. Barbed wire fence bearing E-W and an old fence bearing N.


Set 30" iron pipe 24" in the ground alongside original corner stone.

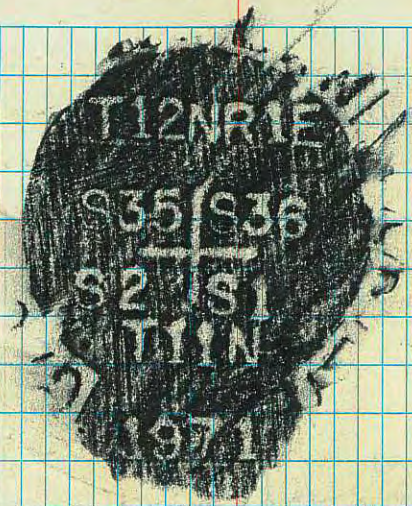

Re-Marked W



10-9-71

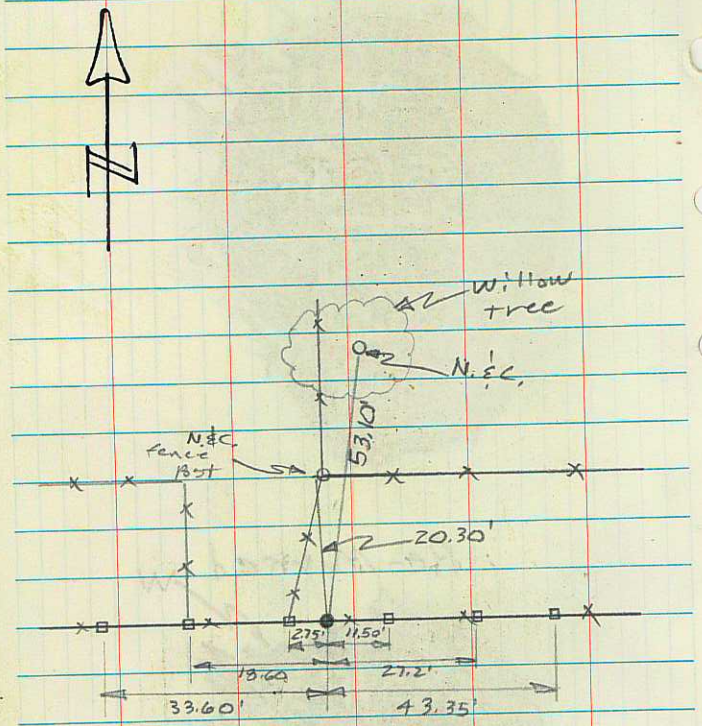

□ - Steel fence Posts

6-8-71 3

#2

NE. corner Section 10

T10N, R1W

10-27-72


A limestone Rock 21x12x10 ins. firmly set and very plainly mkd. with 5 Notches on South and 2 Notches on East faces.

On East side of N-S Road under barbed wire fence bearing N-S.

Set a 30" Steel Pipe 24" in the ground alongside original corner Stone with concrete at bottom and to form a collar around Stone and I.P.



#2

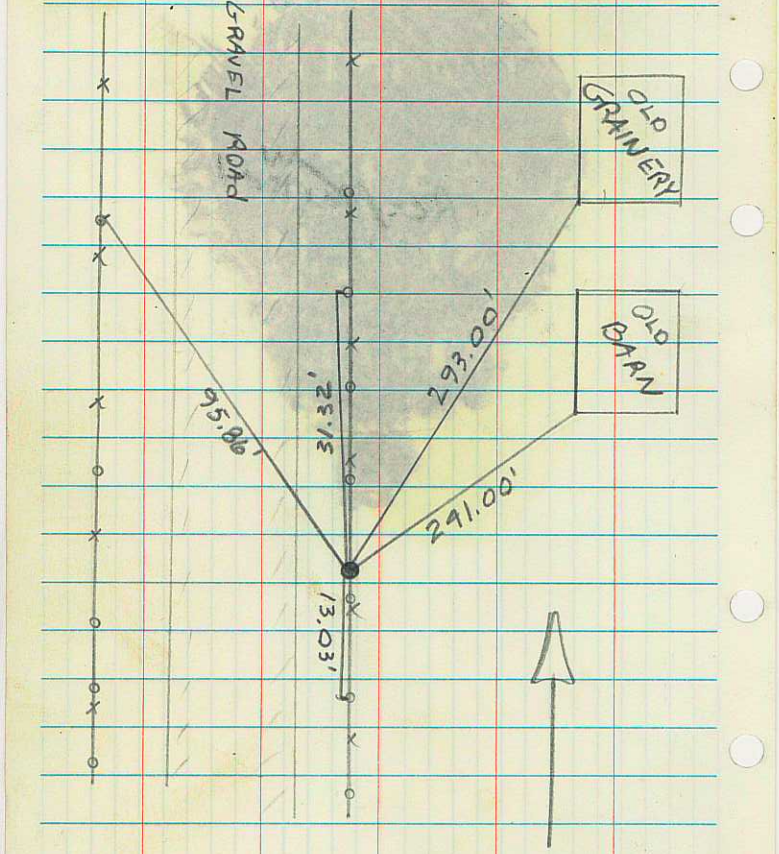

6-8-71 5

#3

NE corner of Sec. 9 T10N, R1W

10-27-72


A Limestone 18x12x10 ins, firmly set and very Plainly mkd. with 5 notches on South and 3 notches on East faces and an "X" on top.

150' West of Wellsville-Mendon Lower canal on E-W barbed wire fence.

Set a 24" I.P. flush with ground at the exact point of "X" on top of rock. Replaced original rock alongside and East of I.P.



#3 7

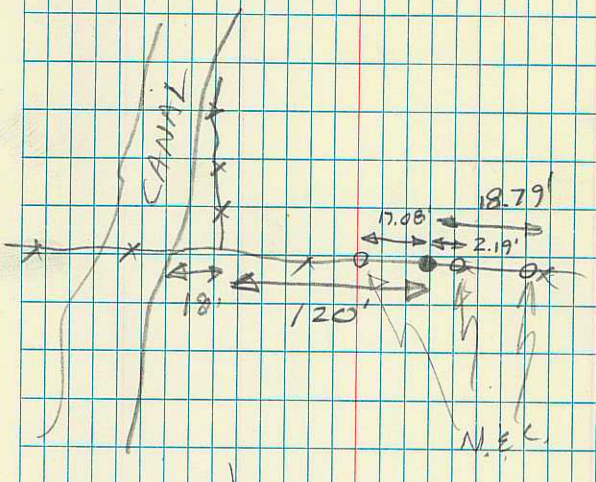

6-12-71 8

#4


East 1/4 cor.


Sec. 16

T10N, R1E.


✓ 10-27-72

A Sandstone 16 x 10 x 7 ins. firmly set and very plainly Mkd. 1/4 on West face. Re-Bar alongside. set References to Re-Bar. Set 24" I.P. 18" in ground in place of Re-Bar alongside original Rock cor. with concrete in Bottom of hole and to form a collar around I.P. & Rock. corner in 30' East of N-S oil road.



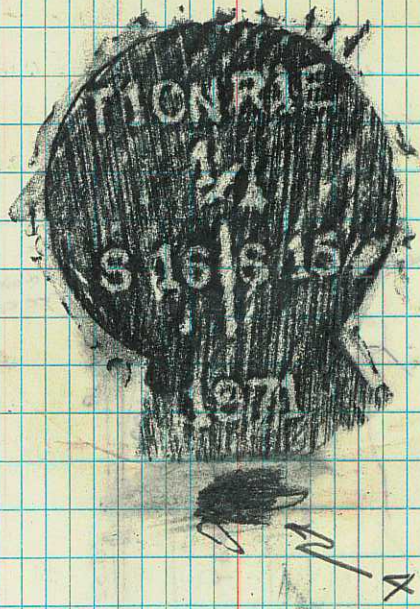

#4

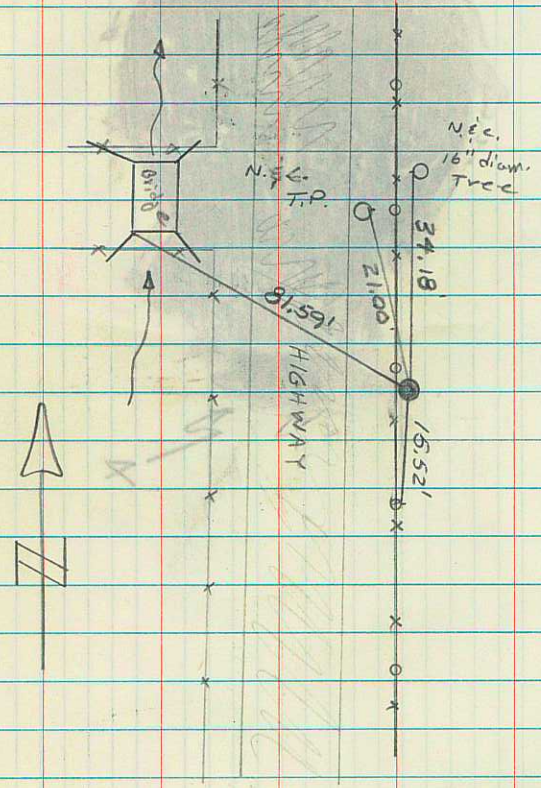

10


#5

NE corner Section
24
T10N R1W


10-27-72

A nail in center of N-S gravel Road. Set by E. Moser, with reference Stakes.


Set 12" I.P. 8" under surface of gravel in concrete at exact point of nail.

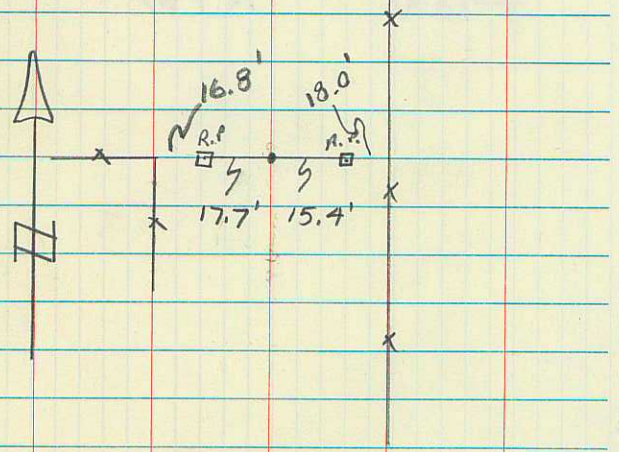



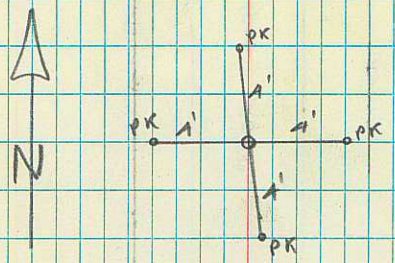

#5

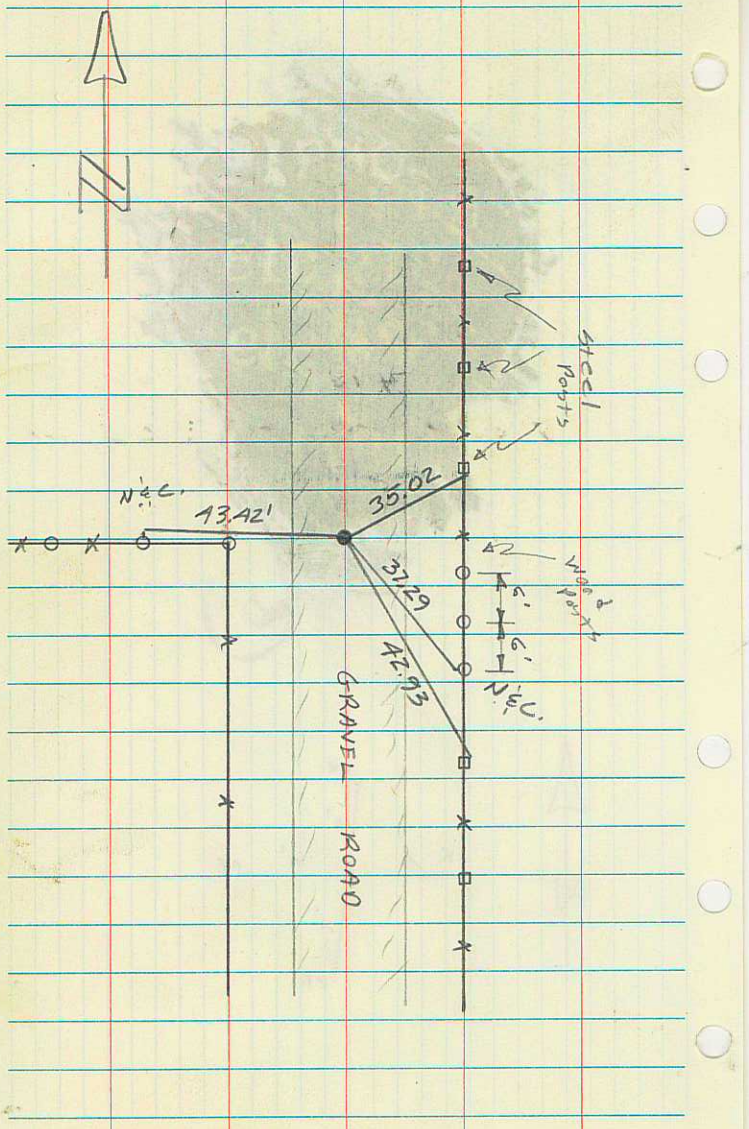

6-16-72

#6


NE corner section 21

T10N, R1W

✓ 10-27-72

A sandstone 20 x 14 x 6 ins. firmly set & very plainly marked with 3 notches on South and East faces. Set 2½" I.P. 24" long 18" in ground alongside original corner stone. Place a collar of stone around Brass Cap.



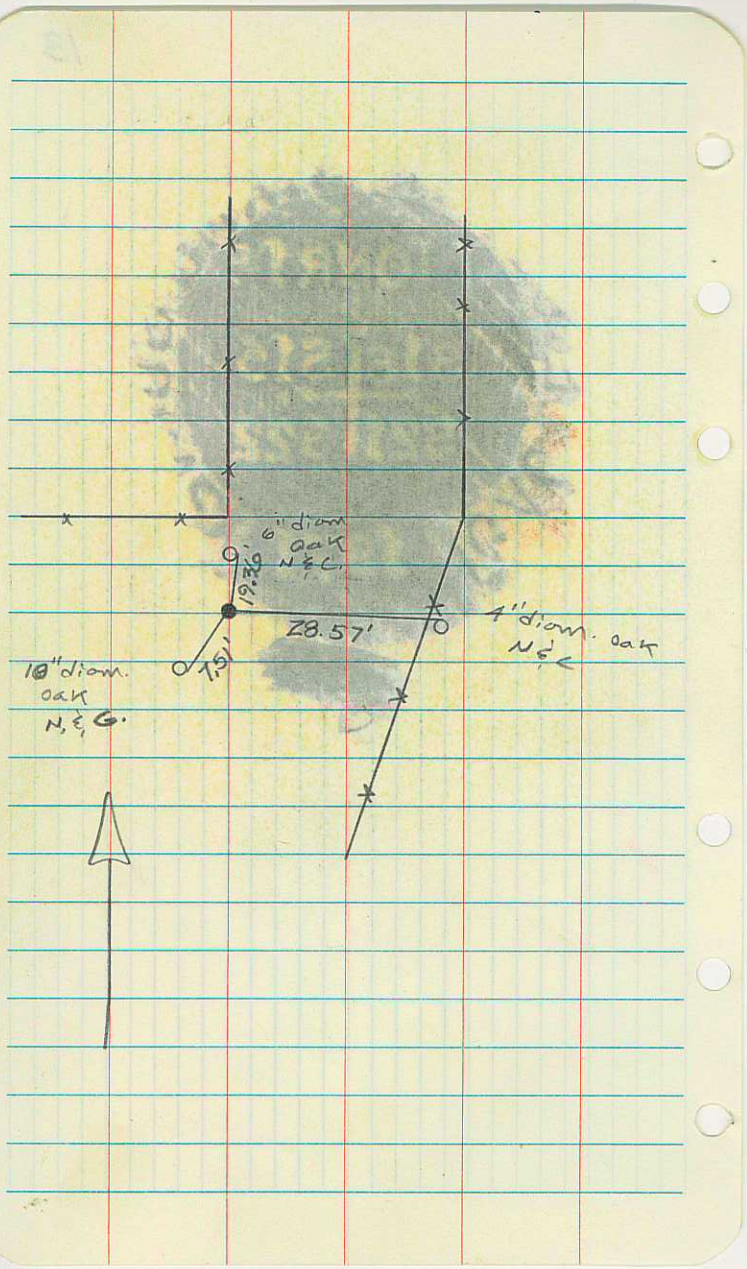

14

6-22-71

#7

North 1/4 corner

Section

26


T13N, R1E

10-27-72


A Re-bar set by Valley Engineering at corner of fence. Fences bearing South and West.

set a 2" I.P. 30" Long 24" in ground with 8" of concrete at bottom of pipe, 12" of rock and a collar of concrete 4" thick at ground level.


placed Re-bar and steel fence post alongside I.P. in concrete

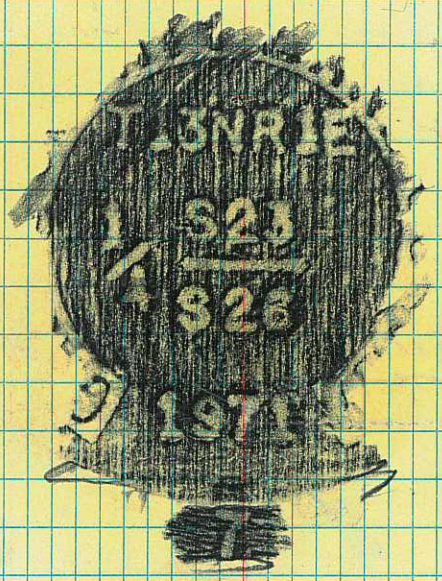

12-6-71

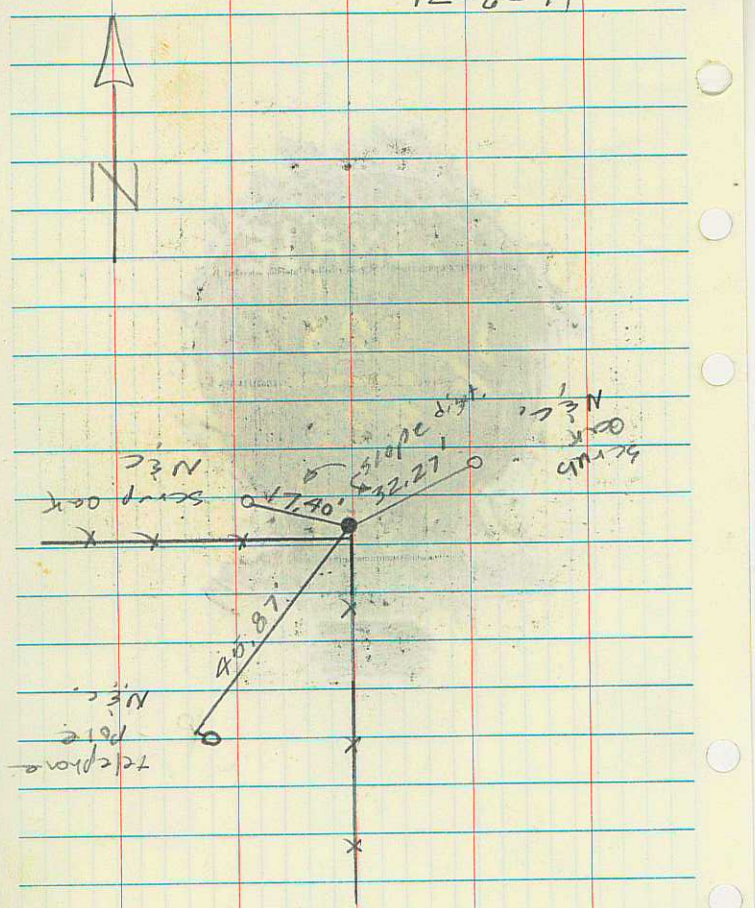

16

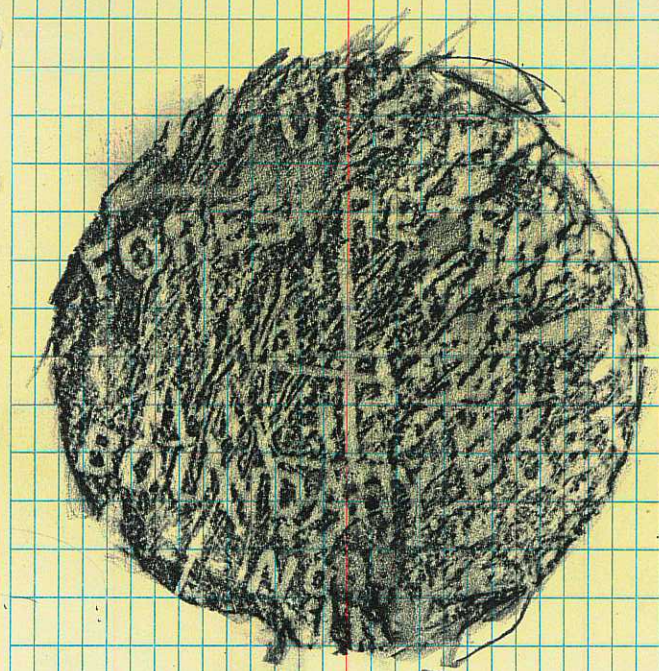

NO. 88

17

6-24-71

#8

East 1/4 corner

Section 23

T13N, R1E


10-27-72

A limestone Rock 12 x 10 x 5 ins. firmly set and plainly marked with a ¼ on West face. A ½" Re-bar set by Valley Engineering was alongside original corner.

Corner is located at the intersection of fences bearing N-S and NE.

After first referencing Re-bar set 2" I.P. 30" long 24" in ground with original corner alongside. Placed 12" of concrete at bottom then 6" of rock and 6" of concrete to form a collar around I.P. and Rock.



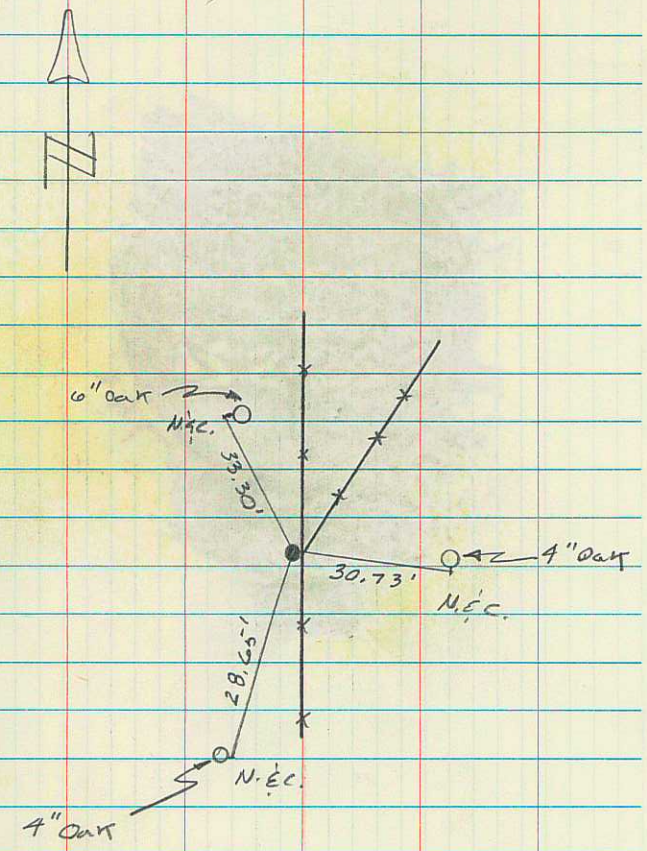

6-25-71

#9

NE corner Section

26

T13N R1E


10-27-72

A ½" bolt assumed to be set by E. Moser at corner of fences fences bearing North and East.

After referencing bolt set 2" I.P. 30" long 24" in ground. Place 12" of concrete at bottom of pipe then 8" of rock and 4" of concrete to form a collar around pipe.



#9

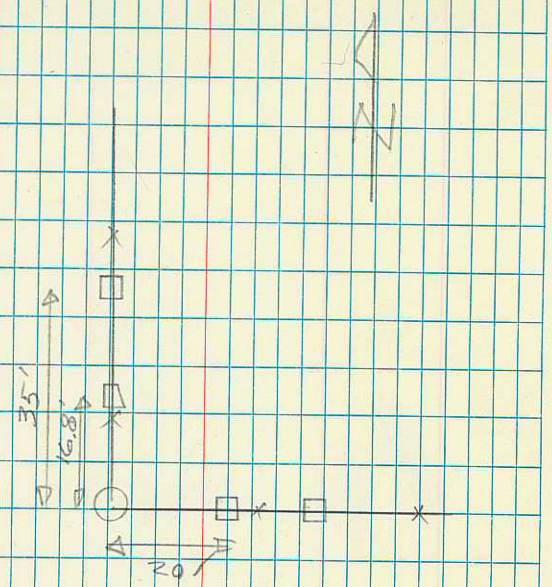

22


6-25-71

#10
NE corner section
27
T13N R1E

10-27-72


A 1¾" Pipe firmly set Approximately 75' South of fence corner, fences bearing North and East & West.

Set 2" I.P. 24" long 20" in ground with concrete at bottom and to form a collar around 2" I.P. and original 1¾" pipe.

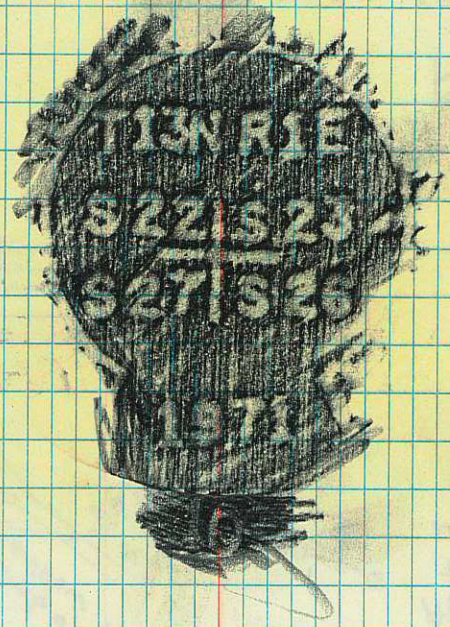

This 1¾" pipe has been the basis for several surveys in the area

12-6-71

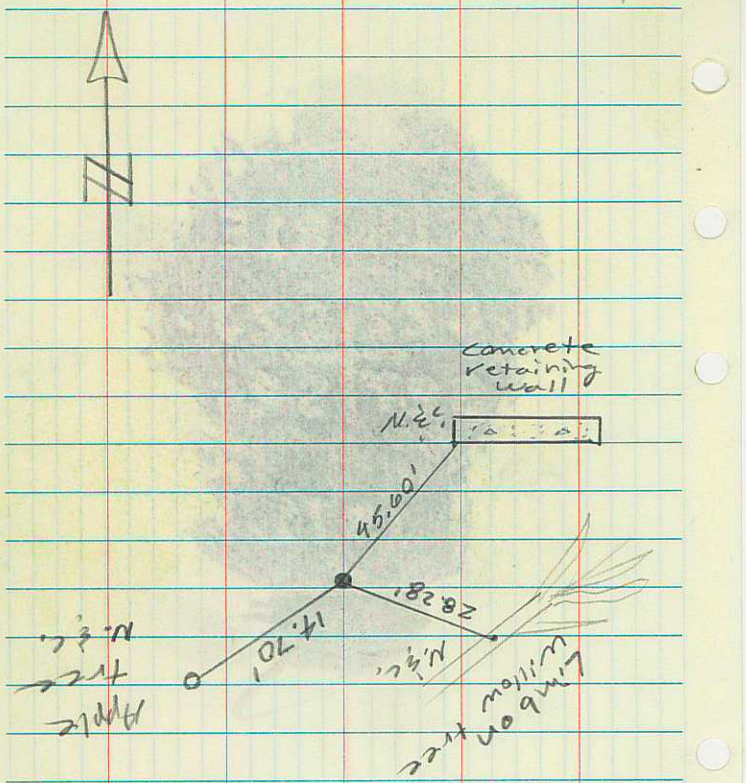

24


6-25-71

#11

N ¼ corner
Section 32
T13N R1E

✓ 10-27-72

A hard gray sandstone perminantly set and mkd:



Could not find any other markings on the face of stone.

Set 2" I.P. 30" long 26" in ground alongside south side of original corner. Place concrete at bottom of I.P. and to form a collar around pipe.




#11

26

93.87

37.45

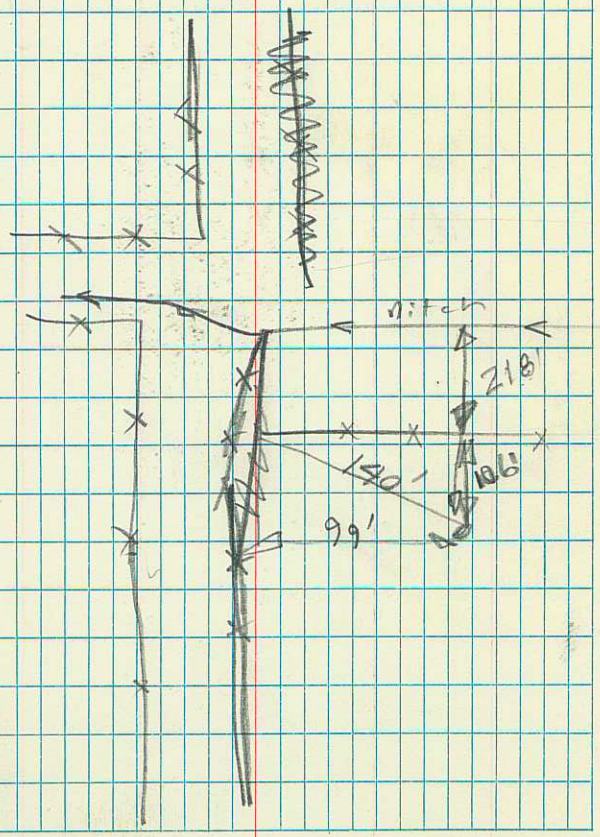

27

6-25-71

#12

East 1/4 corner

Section 29

T13N R1E

10-27-72


A quartzite stationary bolder 16 x 12 ins. at top very plainly marked 1/4 on west face, & an "X" on top.

Corner Located on N-S fence line 12.5' South of Utah Highway # 218.

Set 2" I.P. 30" long 24" in ground on South side alongside original stone, with concrete at bottom and to form a collar around top of pipe. Brass cap 0.55 South of "X"



12-2-71

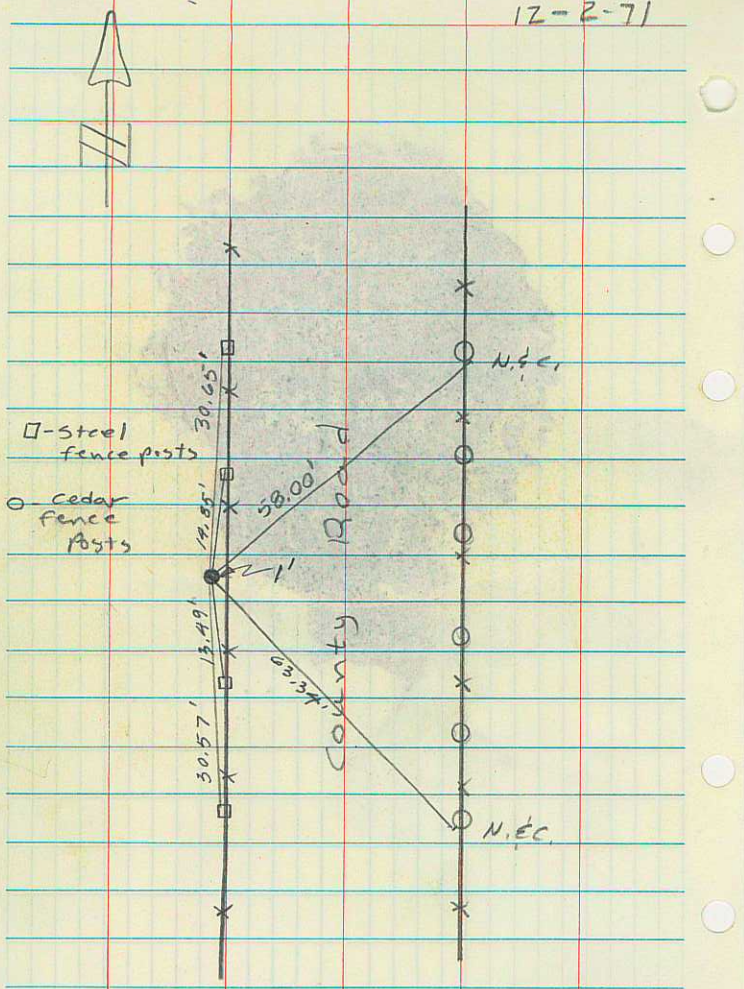

29

6-26-71

#13


East 1/4 corner Section 13

T12N
R1W R1E


✓ 10-27-72

A sandstone bolder 16 x 12 x 5 ins. firmly set and very plainly marked with a ¼ on East face.


Set 2" I.P. 30" long 24" in ground alongside original corner stone. Place 12" of concrete at bottom of pipe, 9" of stone and 3" of concrete to form a collar around pipe and original corner stone.

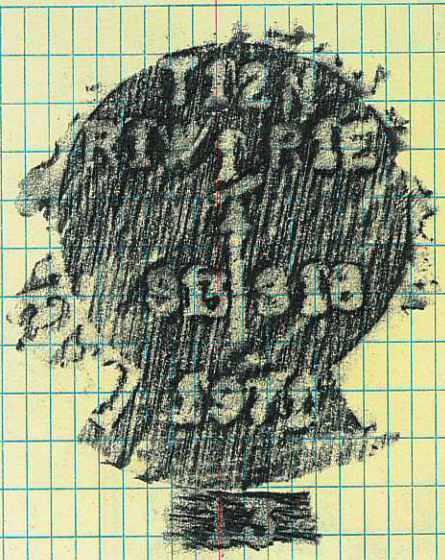

12-23-71

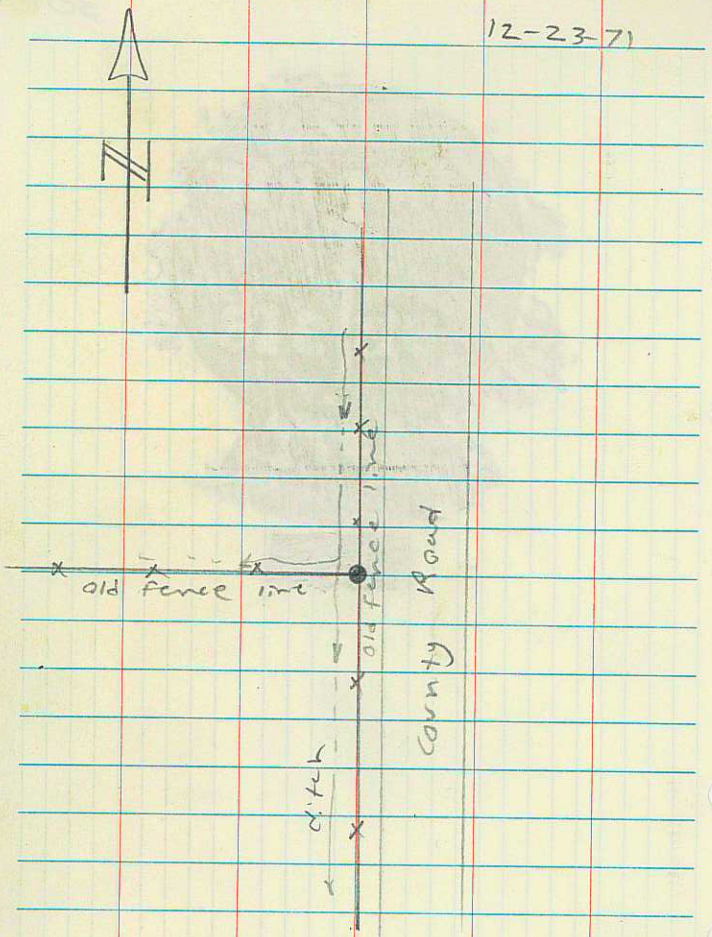
old fence line
old fence line
(county)
ditch

#13 31

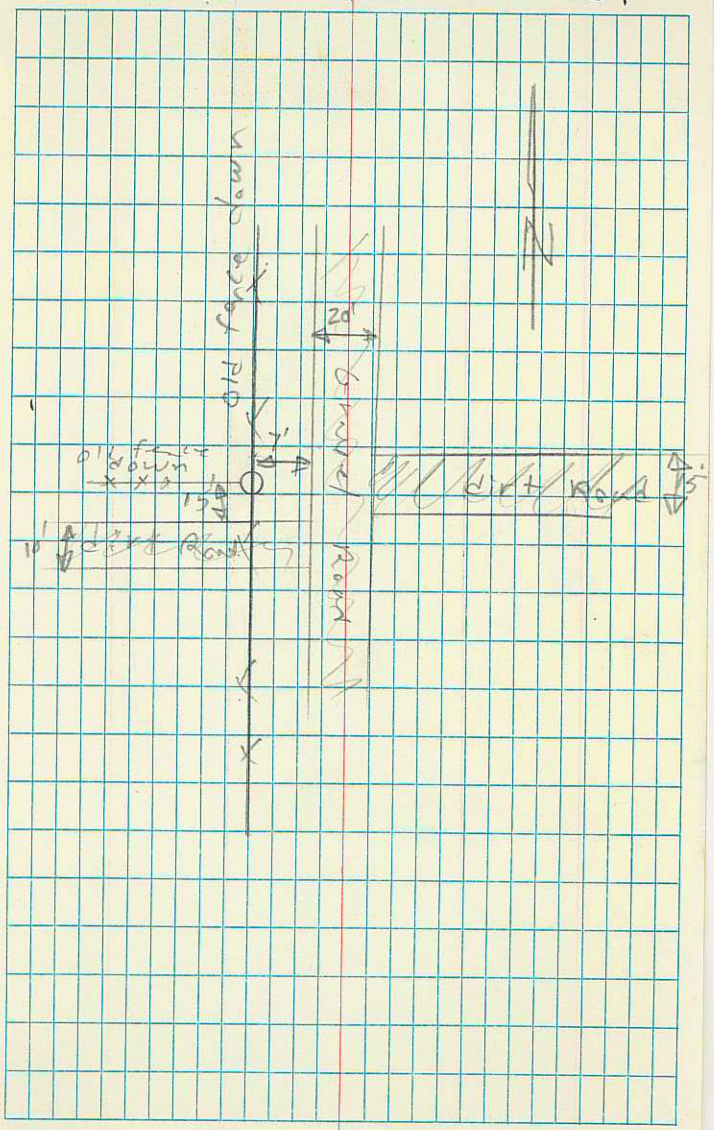
old fence line
20'
old fence line
dirt road

32

30/JUNE/71


14


WEST 1/4 CORNER
SECTION 20
T10N, R1W

✓ 10-27-72

½" X 24" REBAR SET BY VALLEY ENGINEERING ESTABLISED FROM BREAK DOWN OF SECTIONS 17, 20, & 29 IN THE FALL OF 1970 ACCORDING TO B.L.M. PROCEEDURE.

REBAR REFERENCED AND 30" IRON PIPE SET 10" ABOVE GROUND.

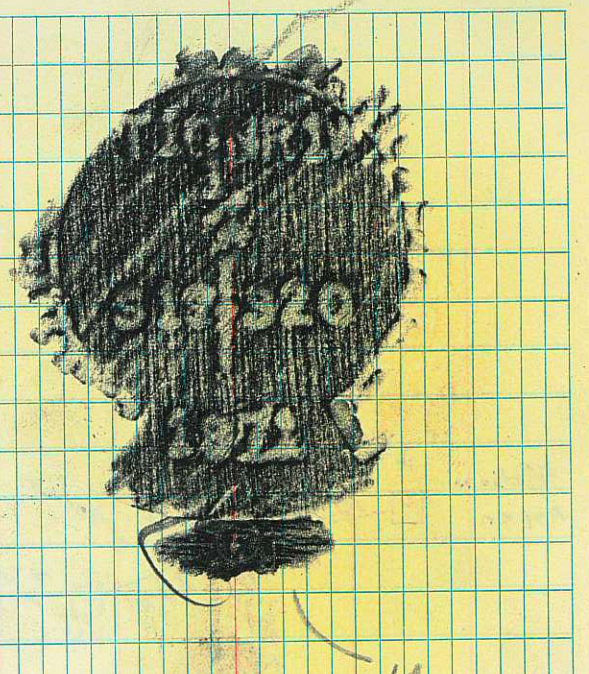

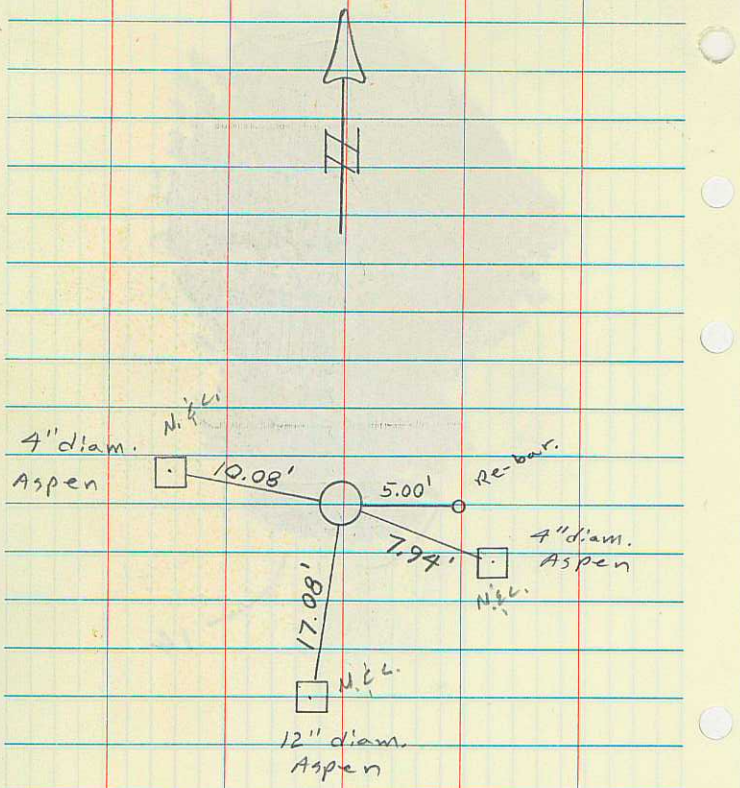

7-19-71 34

#15

NE corner
Sec. 1
T14N R1E


10-27-72

FOUND A 13"X 10"X 7"
QUARTZITE ROCK SET
FLUSH W/ GROUND. SIX
NOTCHES ON ALL FOUR
CORNERS. COVERED
BY A MOUND OF STONES.

SET 2"X24" PIPE W/
BRASS CAP. ± 10" ABOVE GROUND


CONC. FORMS COLLAR
AROUND PIPE & ORIGINAL
ROCK.

MOUND RAISED IMMEDIATELY
WEST OF COR.

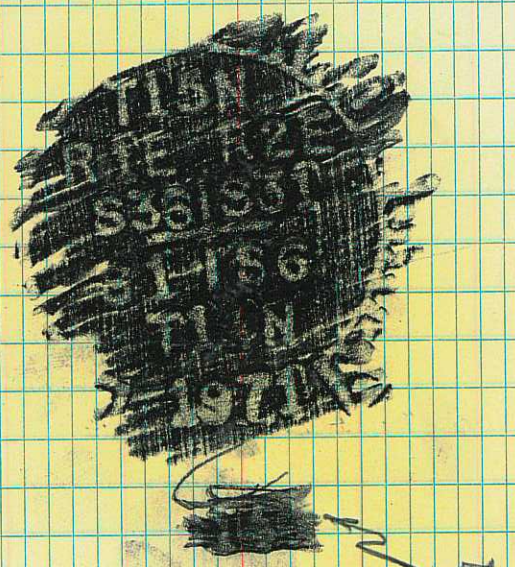

Changed to #15

#15 36

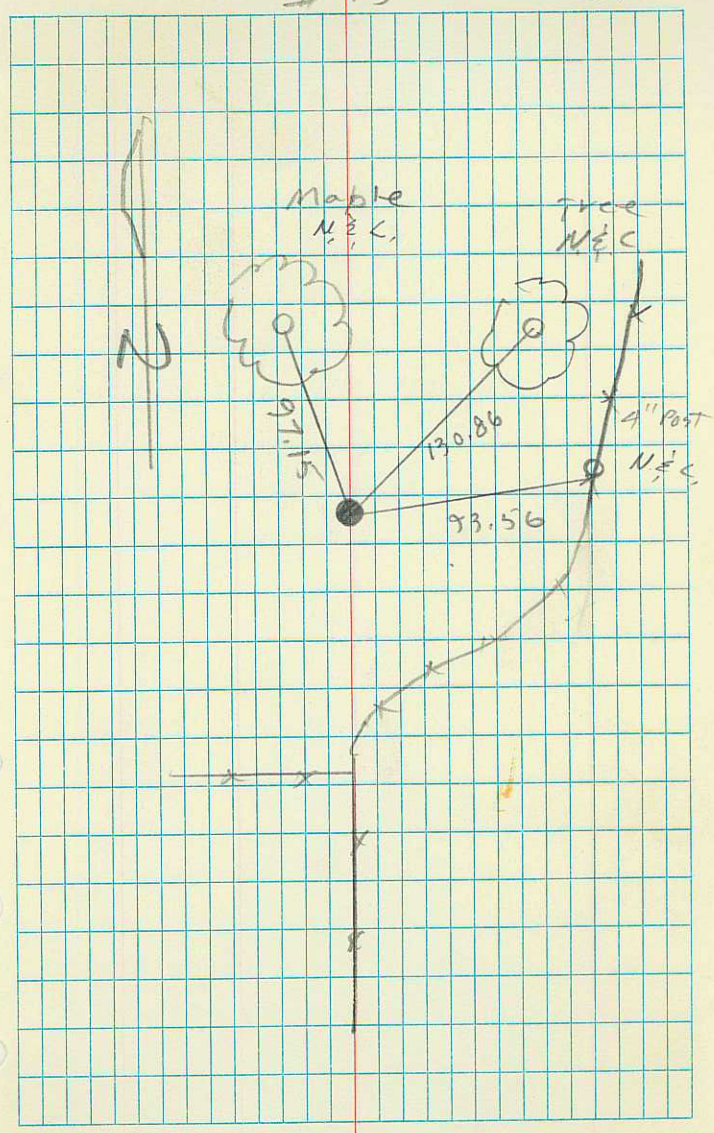

7-20-71 37


#16

North 1/4
Section 6
T14N R2E


✓ 10-27-72

Found a Sandstone 14X10X8 ins. firmly set but no visible markings at intersection of fence.

Set 2" I.P. 30 ins. long 24" in ground with concrete at bottom and to form a collar around I.P.

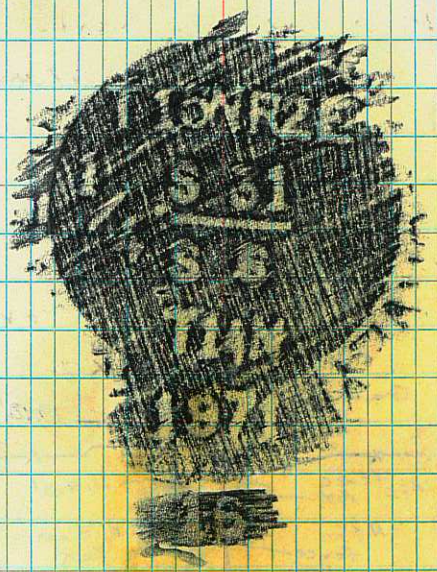

8-10-71

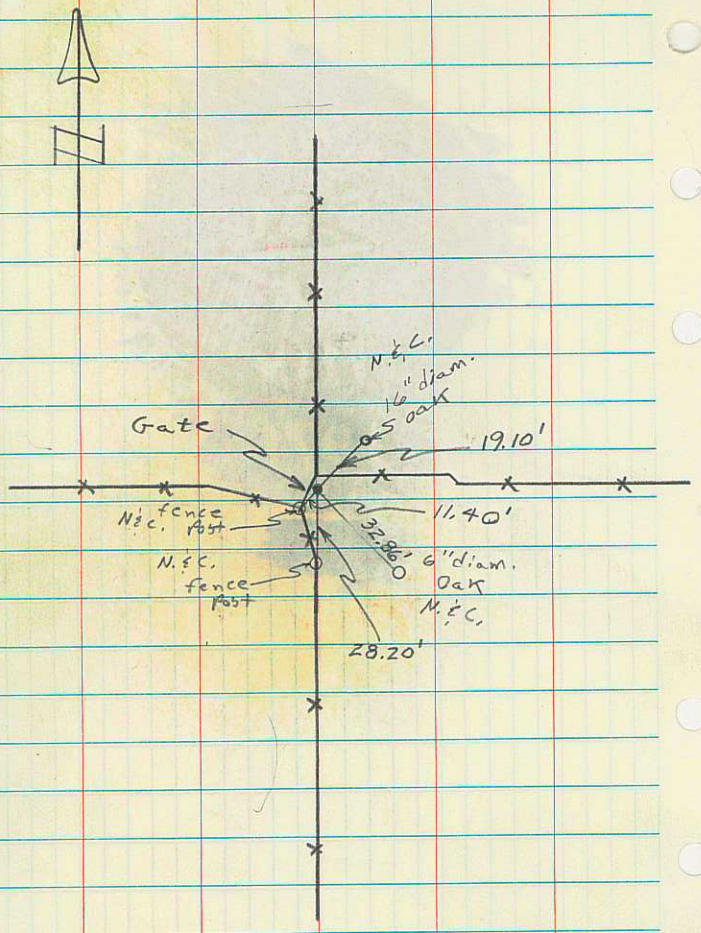

#17

NE corner

Section 13


T12N R1W

Found 1" Galv. pipe with cap firmly set. Corner established by F. Moser.

Set 2" I.P. 30" long 24" in ground with concrete ~~set~~ bottom and to form a collar around both I.P.'s.




12-23-71

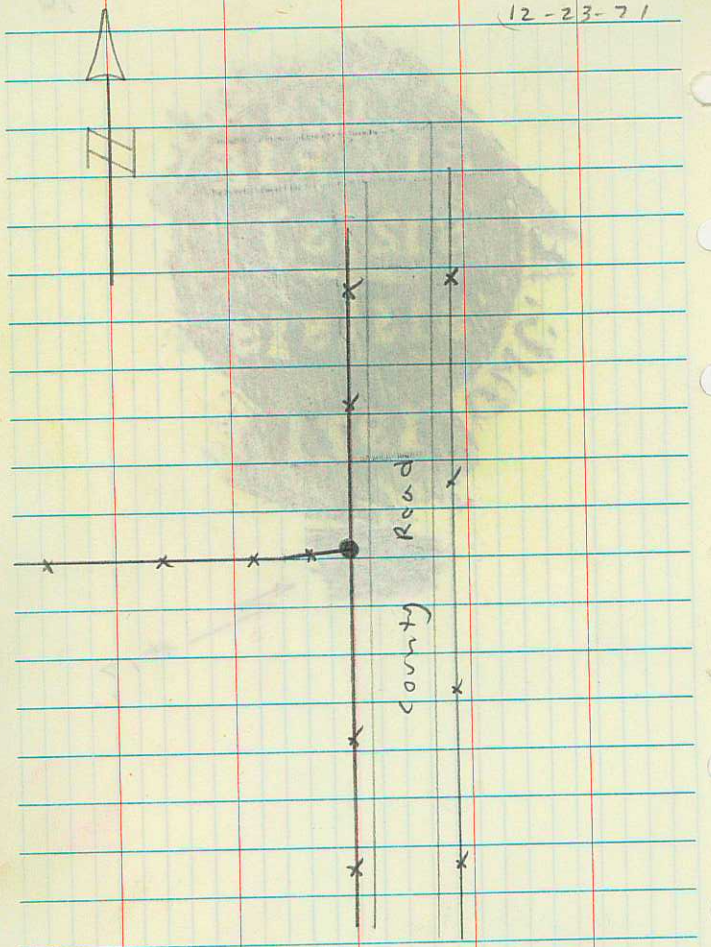
County
Road

#17

41

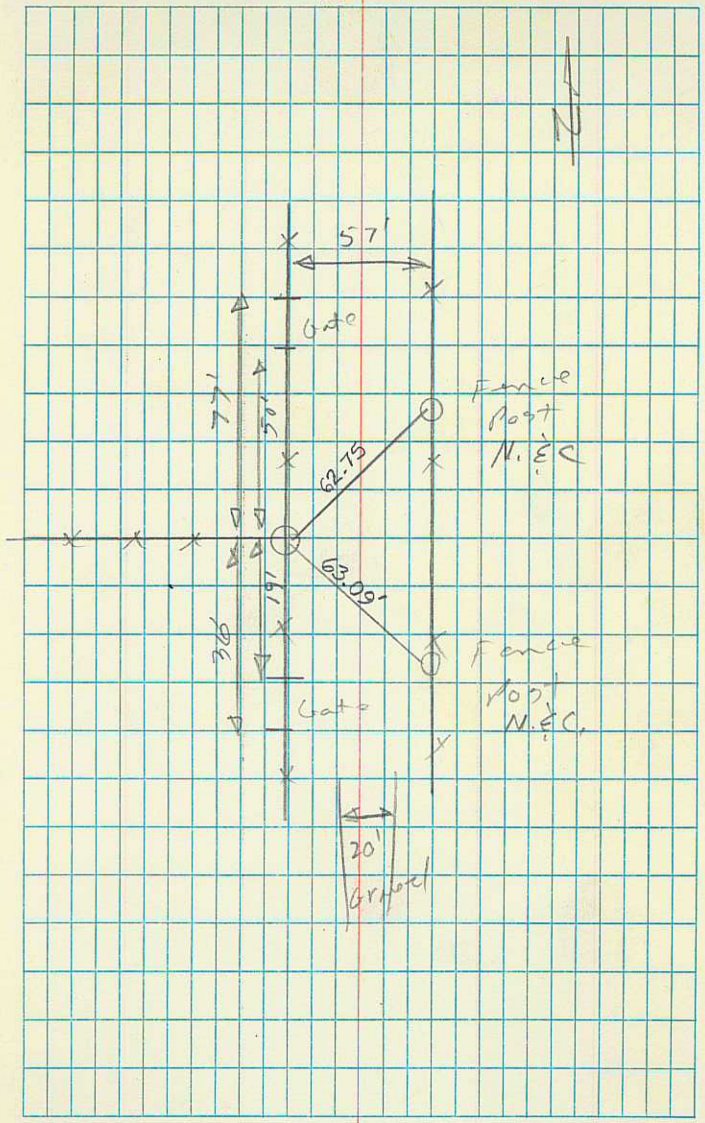
N
57'
Gate
Fence
Post
N.E.C.
62.75
63.09'
50'
19'
30'
Gate
Fence
Post
N.E.C.
20'
Gr. Hotel

8-28-44


#18

NE CORNER
SEC. 17
T13N R1W


10-27-72

Found a Sandstone 31x12x7 ins. firmly set and very plainly marked with 3 notches on East and South edges.

Set 2" I.P. 30" long 24" in the ground with concrete at bottom and to form a collar around I.P. and original cor. stone.

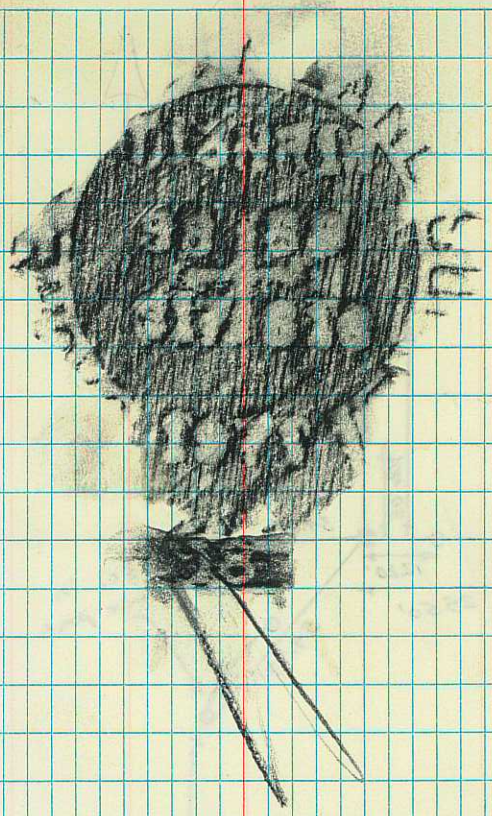

8-30-71

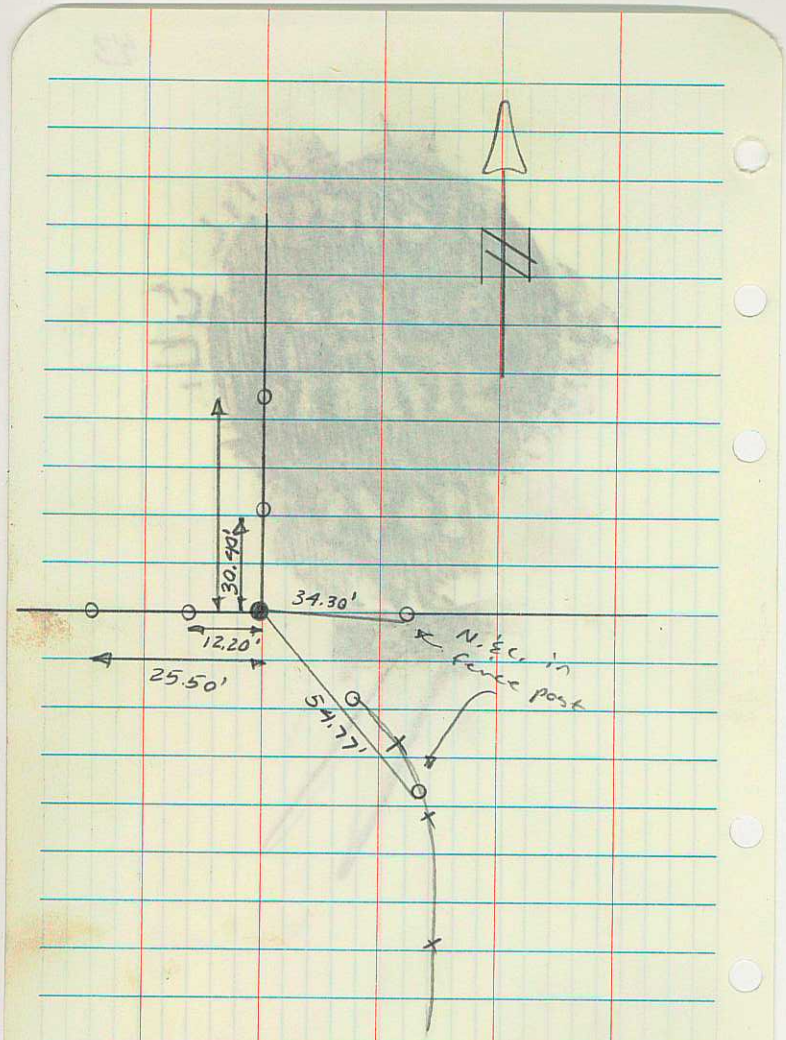


#19


NE corner
Section 1
T13N R1W

✓ 10-27-72

Found a limestone 24x12x8 ins. firmly set and very plainly marked with 3 Notches on South and East edges.

Set 30" I.P. 24" in ground alongside orig. Stone. (no concrete)

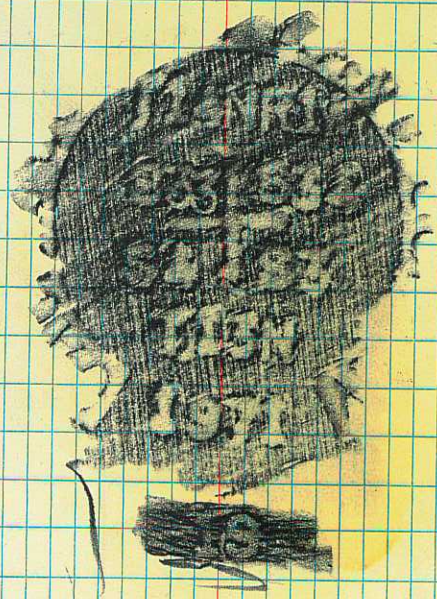

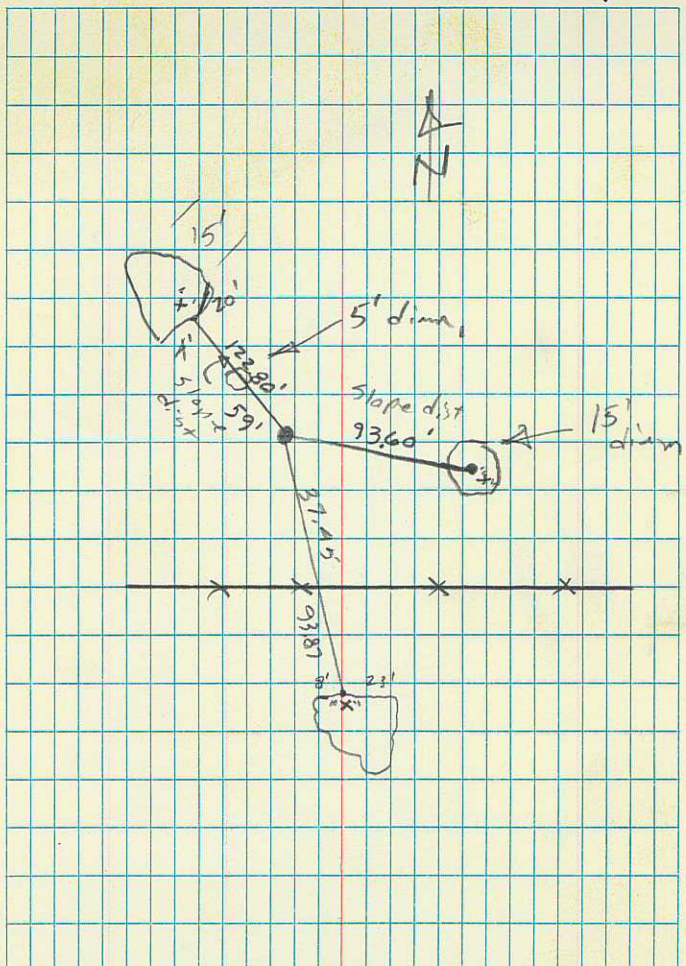
N
15'
5' dia.
slope dist
93.60'
15' dia.
27.45'
93.87'
23'

8-30-77

47


#24

NE CORNER
SECTION 16
T13N R1W

10-27-72


Found a Sandstone 18x6x6 ins firmly set and very Plainly marked with 3 Notches on East and 4 notches on South faces.

Set 30" I.P. 24" in ground along side original corner Stone. (No concrete)

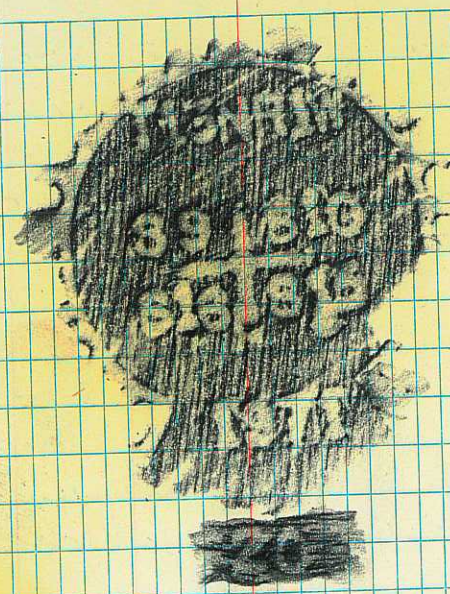

#20

49

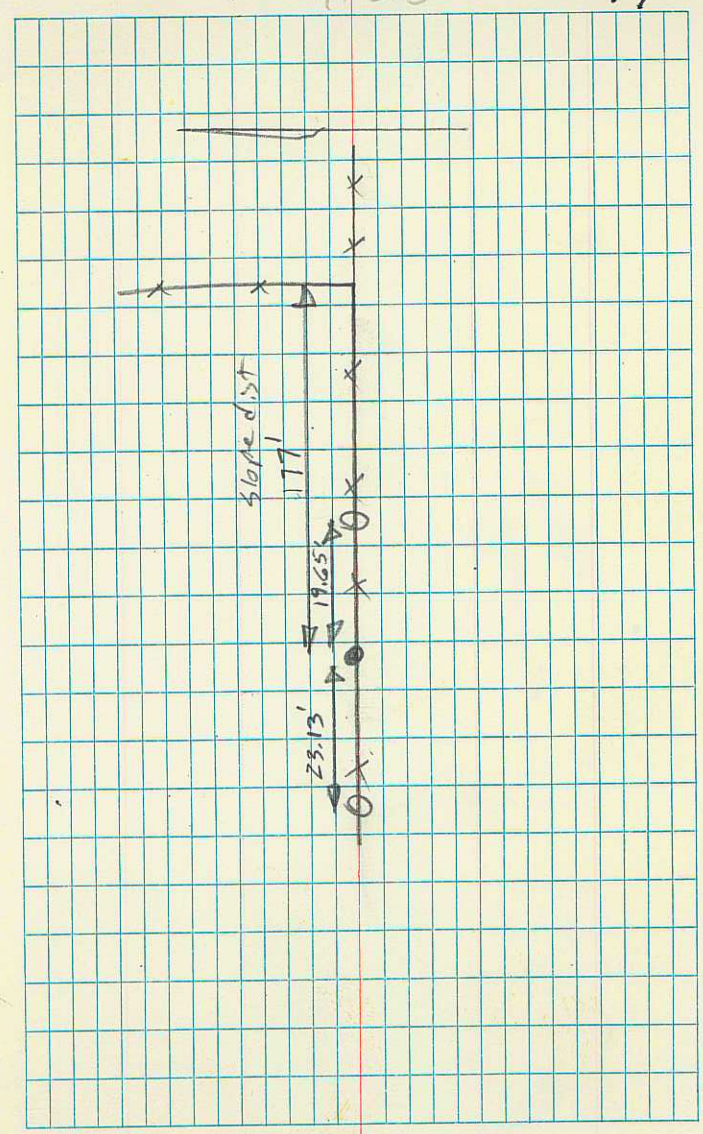

9-2-71 50

#21

N¼ CORNER


SECTION 16


T13N R1W

10-27-72

Found a White lime-stone 18x11x3 ins firmly set and very plainly marked ¼ on West face.

Set 2" I.P. 24" long 18" in ground alongside original stone. Place concrete at bottom and to form a collar around I.P. & stone.

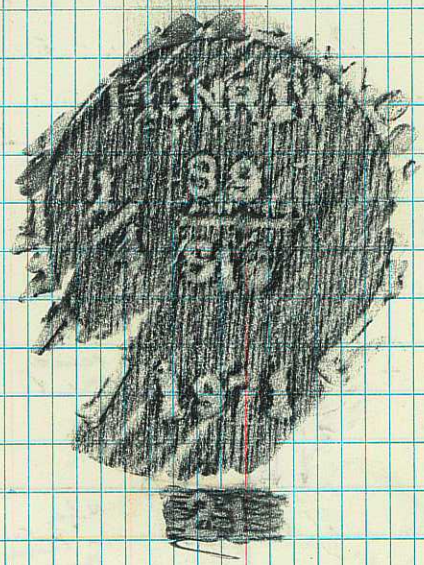

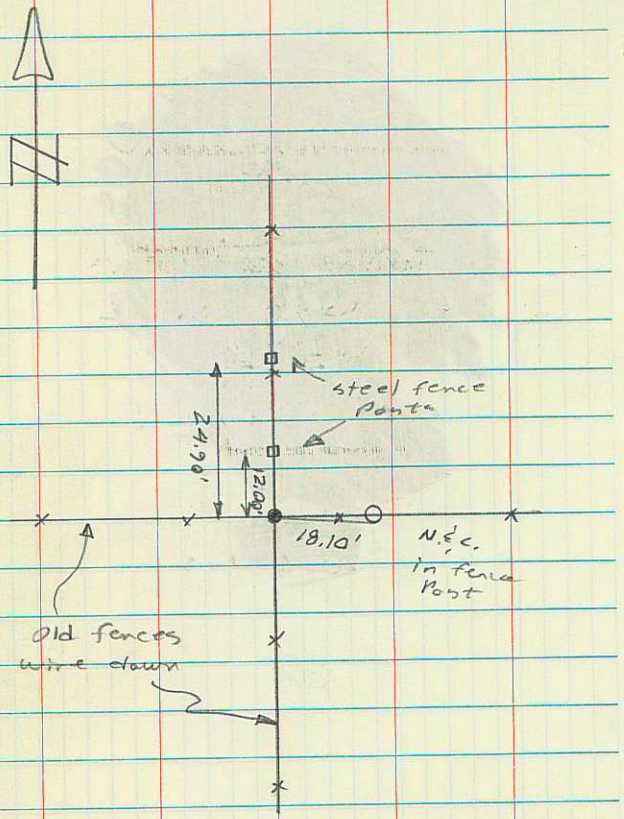

52

9-2-71

#22

NE CORNER

SECTION 9

T13N R1W


10-27-72

Found original corner stone lying loose on ground 4 ft. South and 2 ft. East of fence corner. A Sandstone 16x9x5 ins. very Plainly marked 5 notches on South and 3 notches on East edges.

Set 2" I.P. 30" long 24" in ground at fence corner with original corner stone alongside I.P.



3/16/72

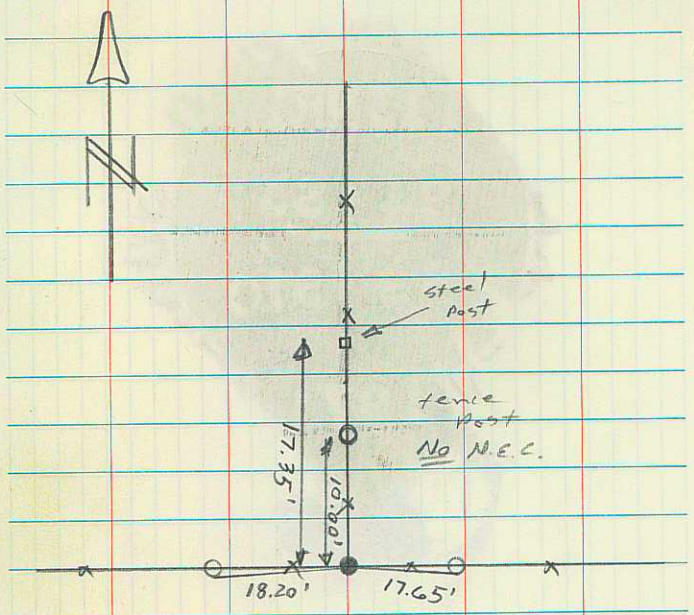


#23

NE 1/16 Sec. 3

T11N, R1E

A cross chisled in the top of a sandstone boulder
Top of stone 6" x 6" square

6-21-72

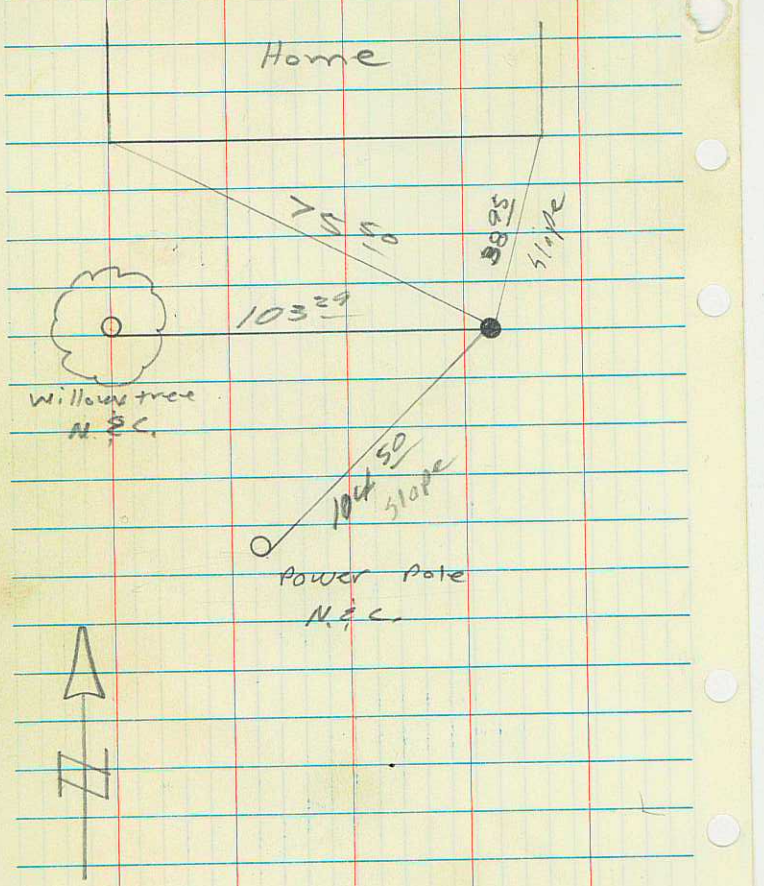

24

NE COR. SEC. 35

T 12 N R 1 E

11-8-72

State Road Brass cap
Set in concrete
18" below ground level
With 4" round valve
box from ground level
to top of brass cap.
box has cover marked
"Water"



58

6-22-72

25

NE. cor. Sec. 2


T11N R1E

✓ 11-8-72

20x16x10

Found a limestone 20"x16"x10" lying loose on ground with No visible markings. Corner was varified by Valley Eng. by ties to old G.L.O. notes.

Set 24" x 1" R. 18" in ground.

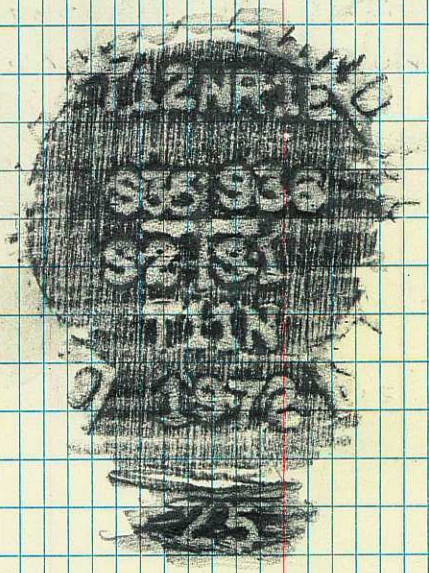

60

6-23-72

#26


E 1/4 COR. SEC. 2

T 12 N R 1 E


✓ 11-8-72

Found a limestone 14x11x5 ins. Firmly set and very plainly mrd. 1/4.

Set 2" I.P. 24" long 18" in the ground Bury orig. ind. cor. stone. Magnetic I.P.

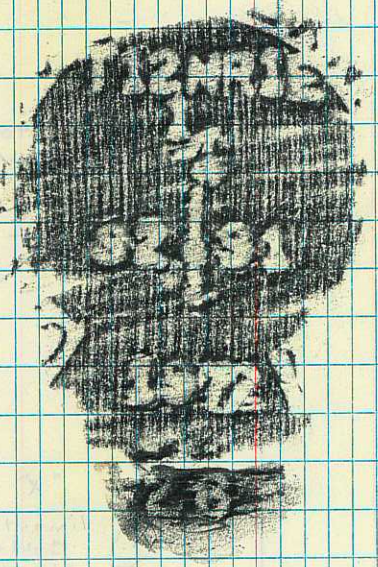

6-23-72

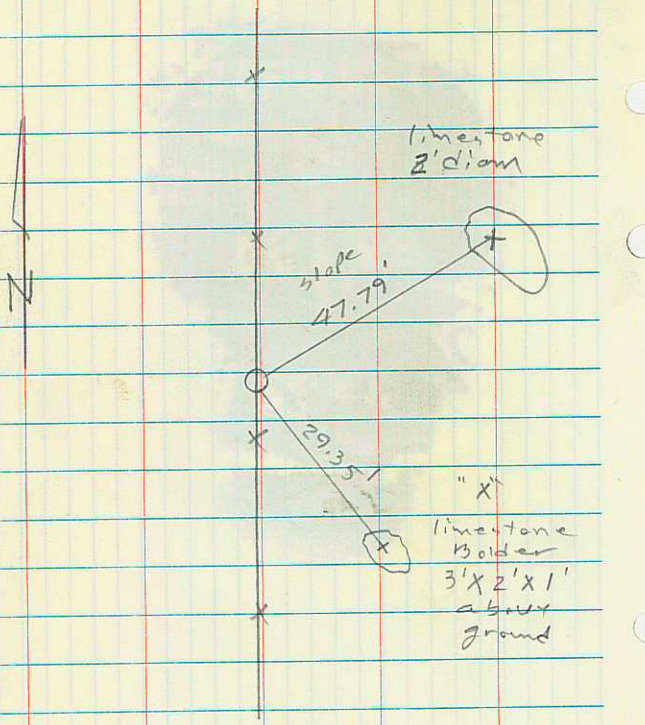

#27


NE COR. SEC. 11


T12NR1E

11-8-72

Found a white limestone 18"x12"x9" boulder firmly set and very plainly marked with 5 notches on N. face and other visible marking.

Set 2" I.P. 24" long 18" in the ground. Bury orig cor stone along side I.P.

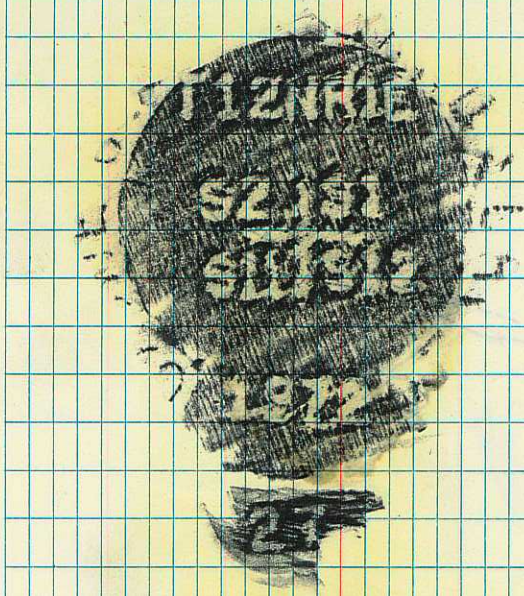

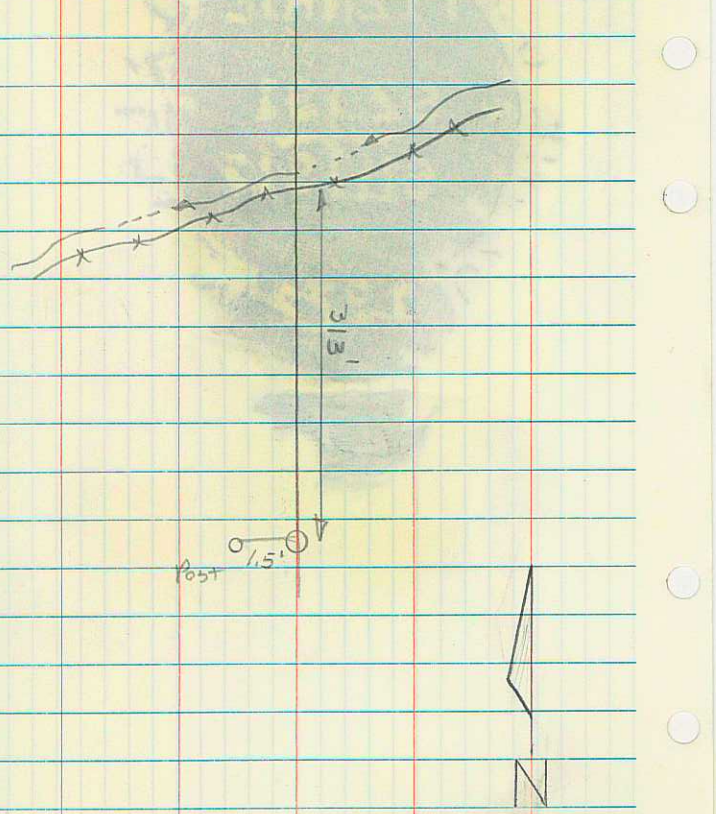

64

6-26-72


#28


NE cor. SEC. 36

T 13N R1E

6-11-8-72

Found 1" I.P. with Brass Cap 33" above ground.

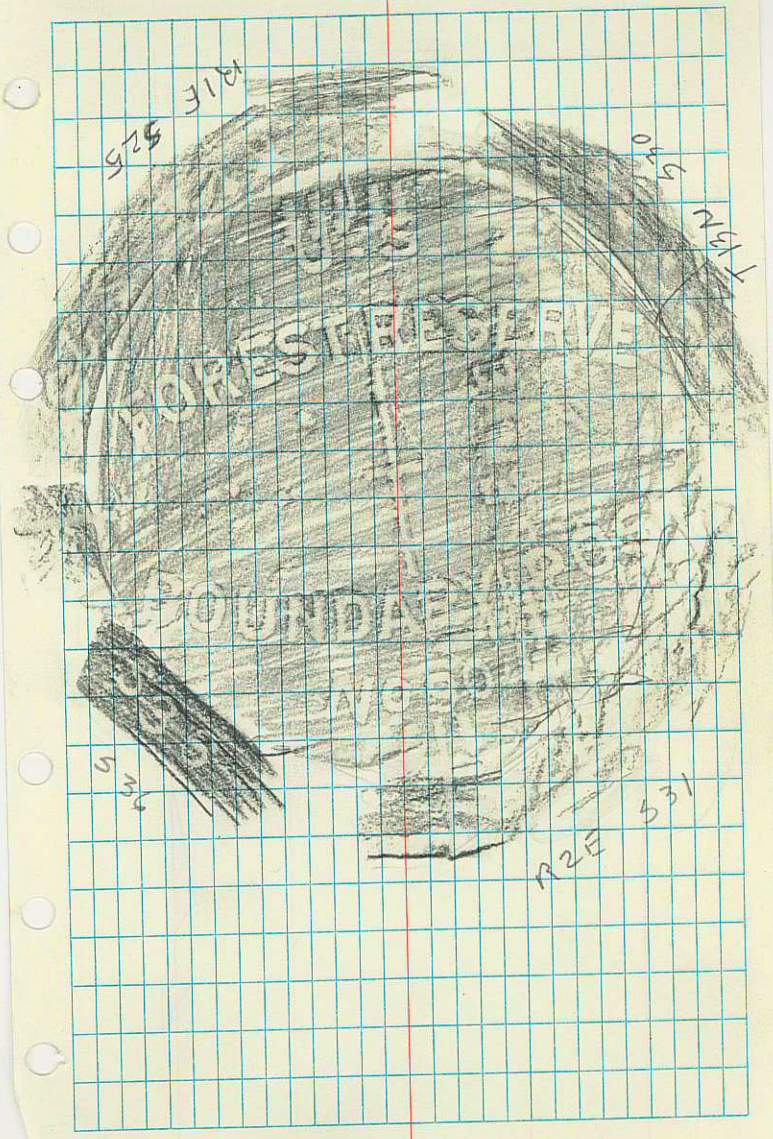

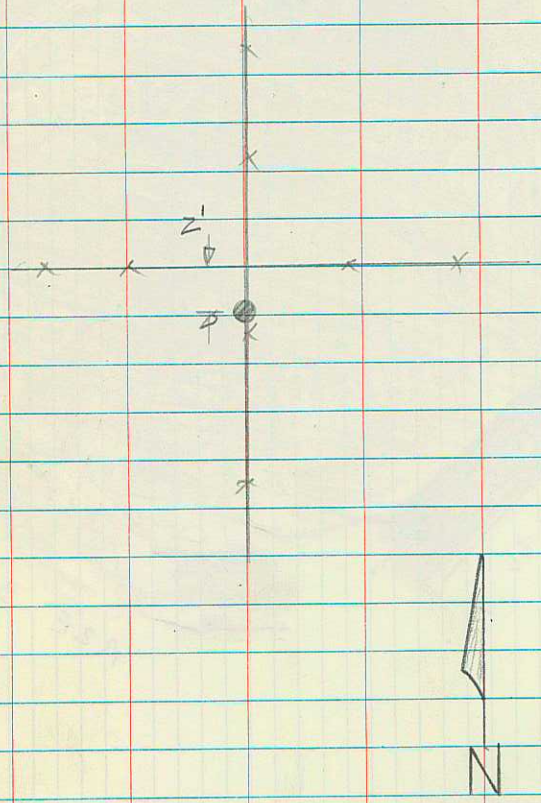

6-27-72 66


#29

NE COR. SEC. 24


T12NR1E

✓ 11-8-72

Found 4" I.P. with brass cap 10" above ground.

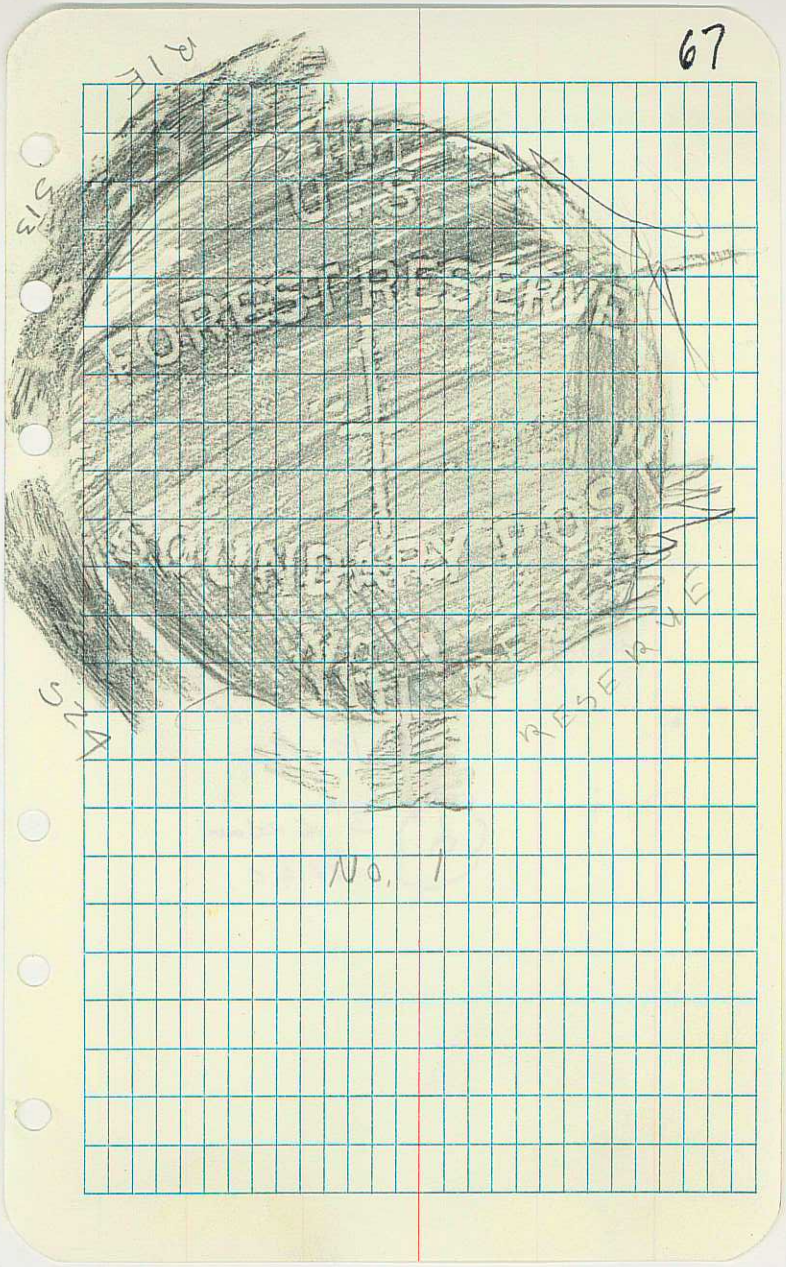

6-27-72

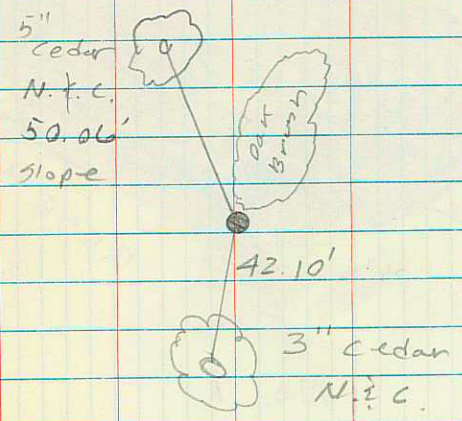


#30


NW COR SEC. 19

T12N R7E

11-8-72

Found 4" I.P. with brass cap. 12" above ground

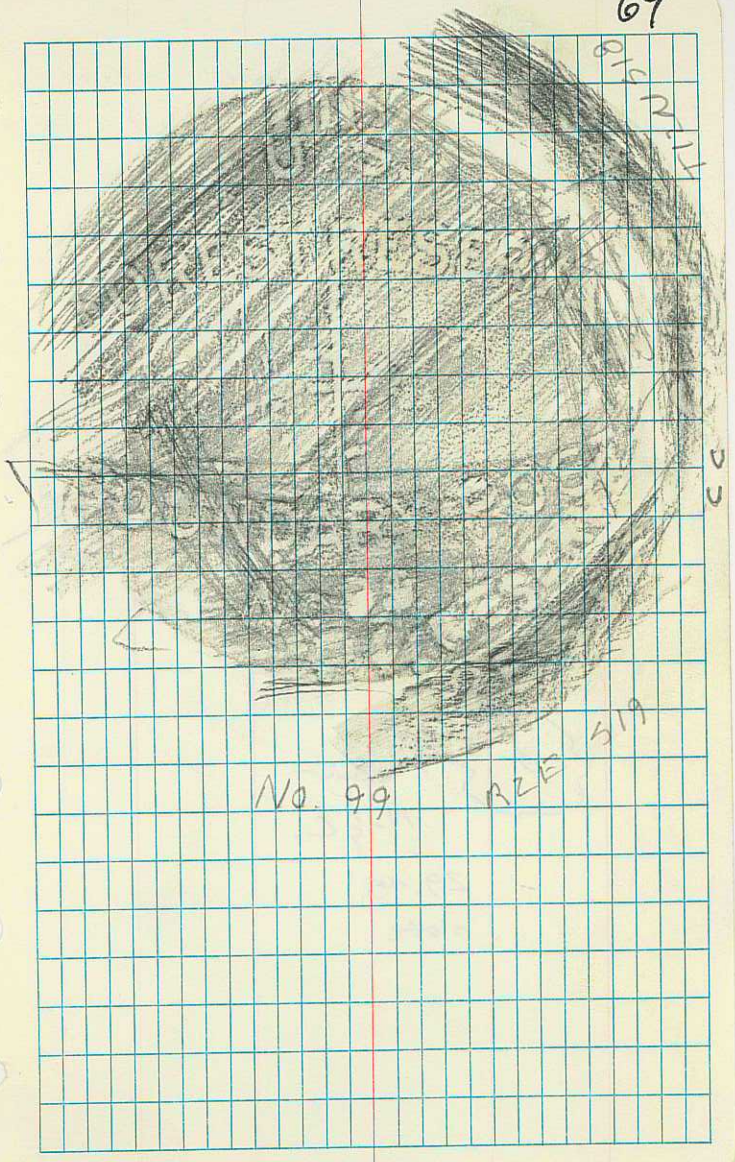

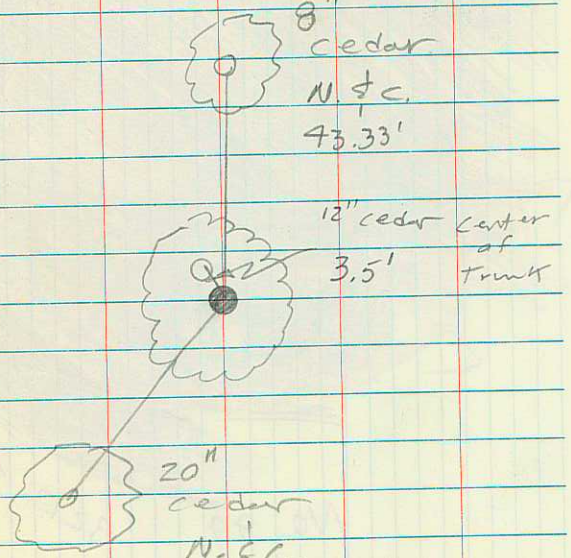

6-18-72

20

#31

NE. COR. SEC. 36

T12N R1E

11-9-72

Found 4" I.P. with brass cap. 3 ft. above ground and mound of stone around I.P.

71

6-18-72

T 32

NE cor. SEC 1

T 12 N R 1 E

11

11-9-72

Found 4" I.P. with brass cap. Mound of Stone around I.P.

72

6-20-72

33

N. 1/4 COR. SEC. 1

T 1 N R 1 E

11

11-9-72

Found 2½" I.P. set by B.L.M.

73

6-30-72

#34

NE cor. SEC. 12

T12N R1E

11-9-72

Found a limestone 21x10x4 ins. firmly set and very plainly marked with 5 notches on S. and 1 notch on N. faces.


Set 2" I.P. 24" long 18" in the ground bury orig. cor. stone alongside I.P.

Raise a mound of stone West of cor.



#34

75

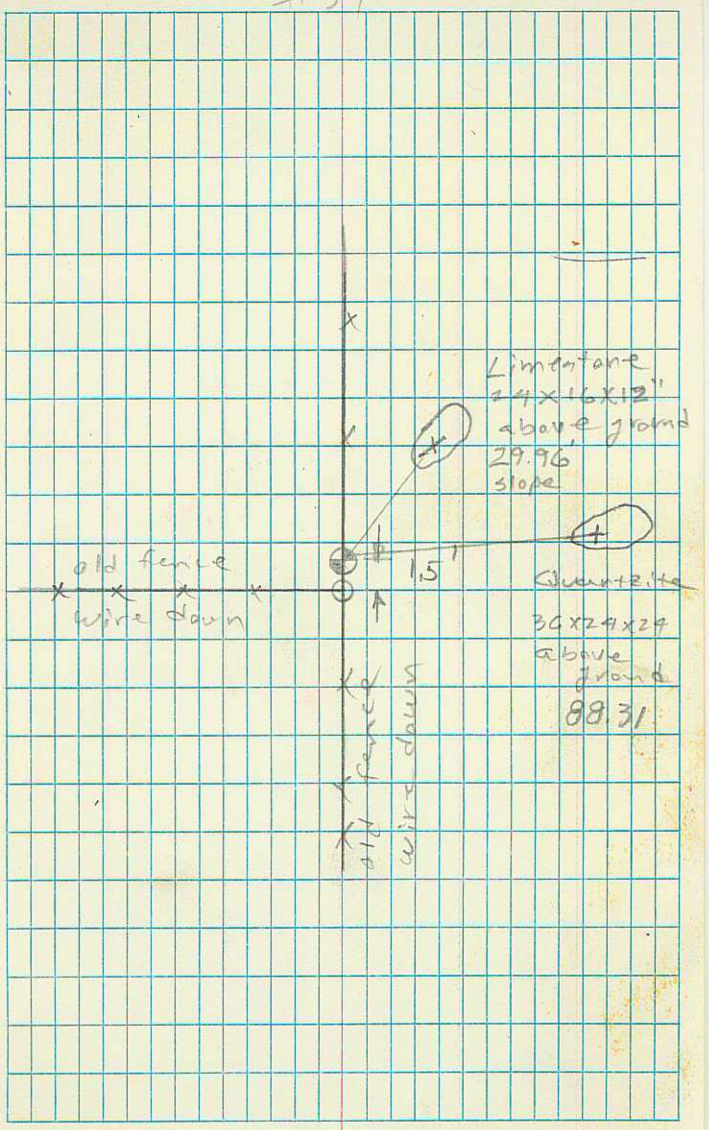
Limestone
24x16x12'
above ground
29.96'
slope
old fence
wire down
1.5'
Sandstone
36x24x24
above
ground
88.31'
wire down

76

6-30-72

#35

E. 1/4 COR. SEC. 12


T 12 N R 1 E

~ 11-9-72

Found a Quartzite Stone 24x18x6" firmly set and very plainly mkd. 1/4 on W. face.


Set 2" I.P. 24" long 18" in ground alongside orig. Cor. Stone

Concrete at bottom of I. P.

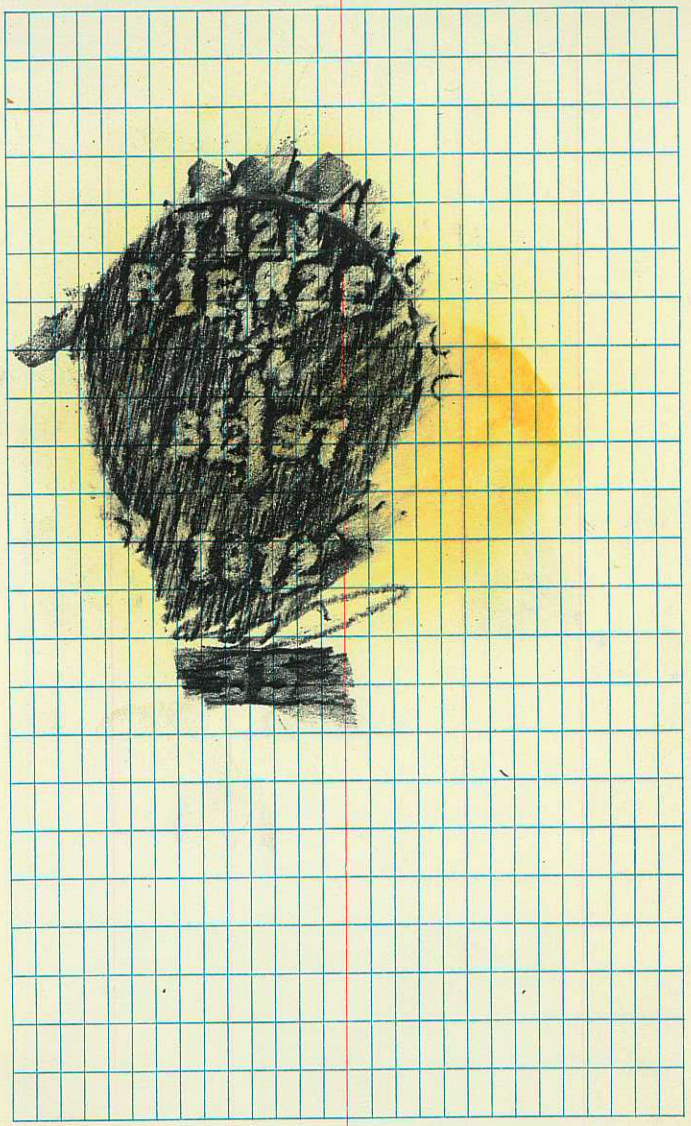

#35

28

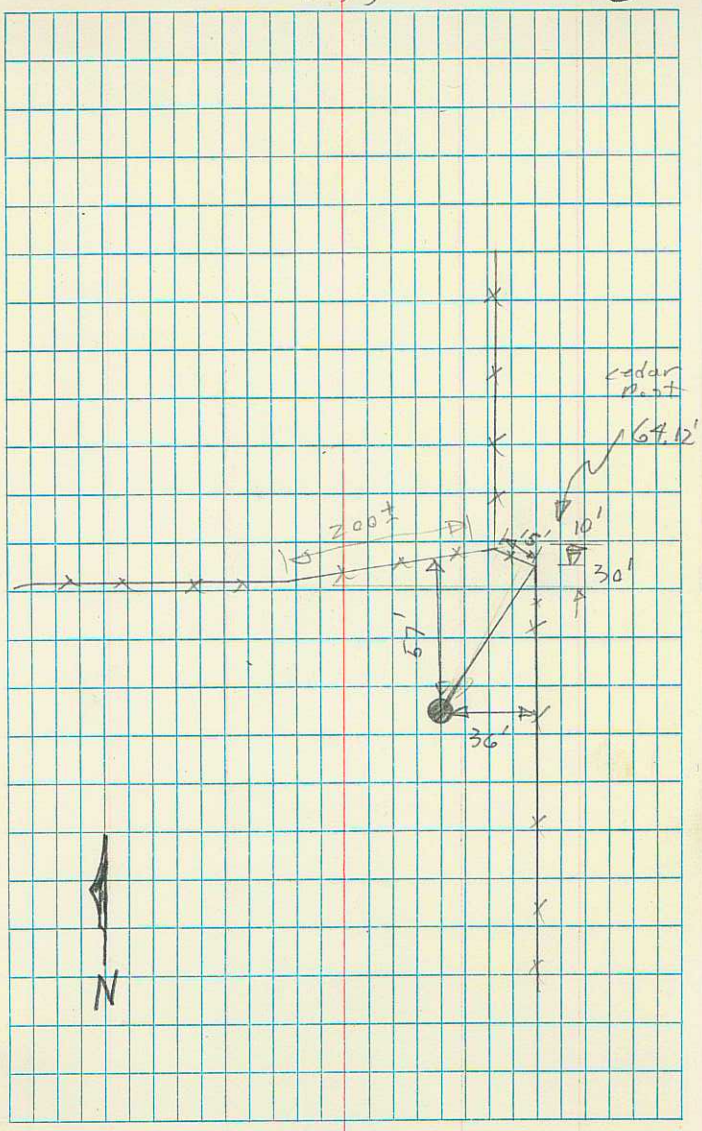

7-6-72

#36


NE COR. SEC. 13

T12N R1E


11-9-72

Found a blue limestone 20x15x3 ins. firmly and very plainly marked with 4 notches on S. and 2 notches on N. faces.

Set 2" I.P. 24" long 18" in the ground. Bury orig. stone alongside I.P.

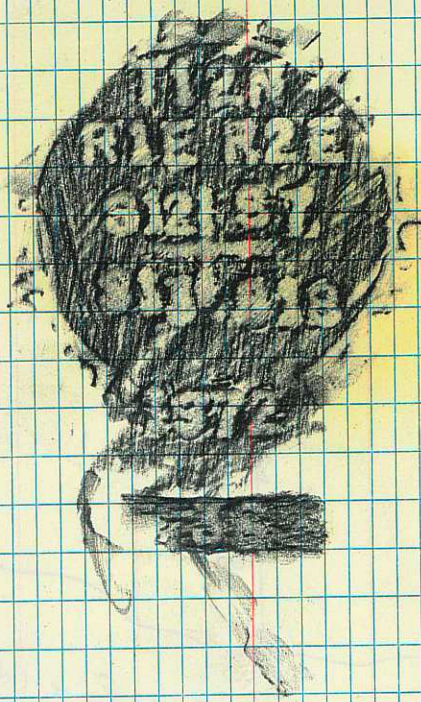

7-6-72

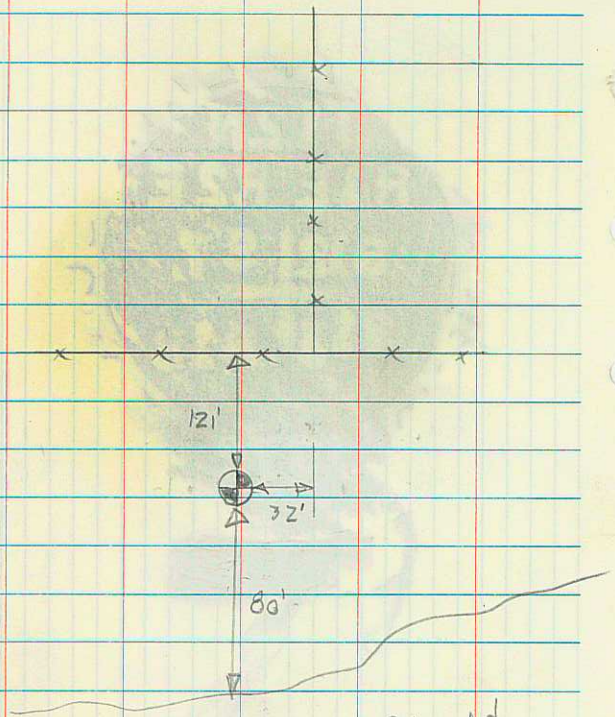


37

NE COR. SEC. 24
T 13 N R 1 W

Found a quartzite stone 15x8x7 ins. firmly set and very plainly marked with 3 notches on N. & S. faces.


Set 2" I.P. 24" long 18" in the ground. Bury orig. lap stone along side I.P.

(No concrete at bottom of I.P.)

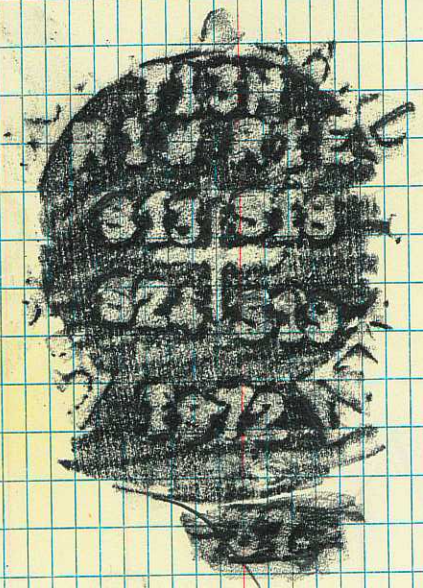

#37

83

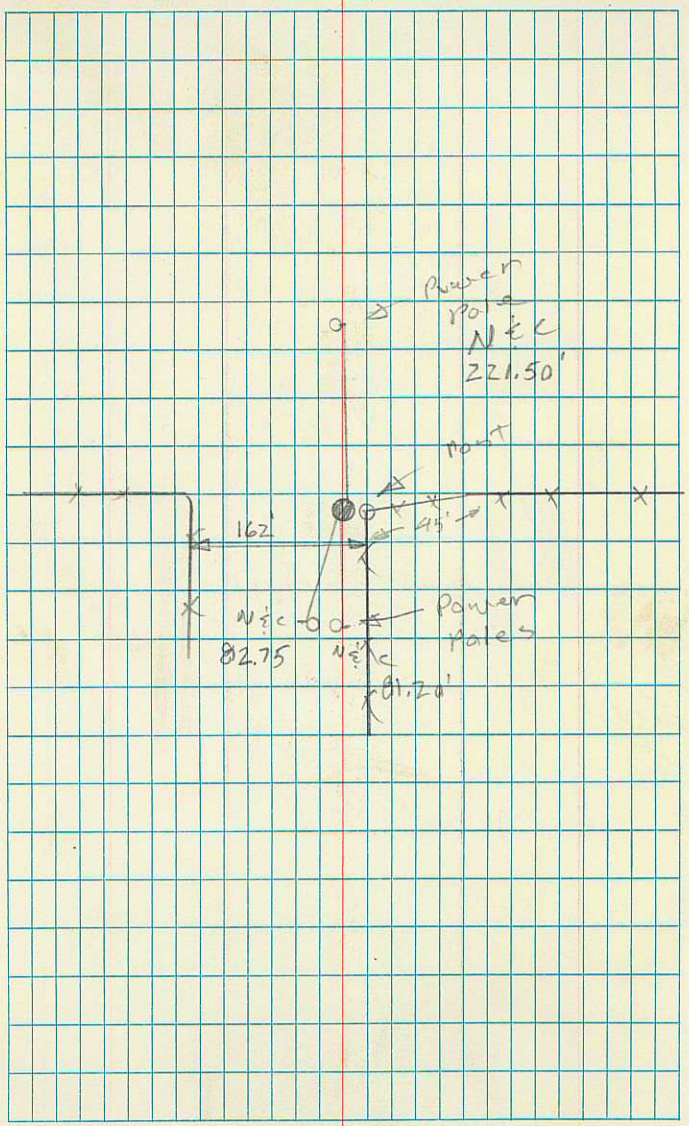

84


7-6-72


#33

E. 1/4 COR SEC 33

T 14N R2W

L-11-9-72

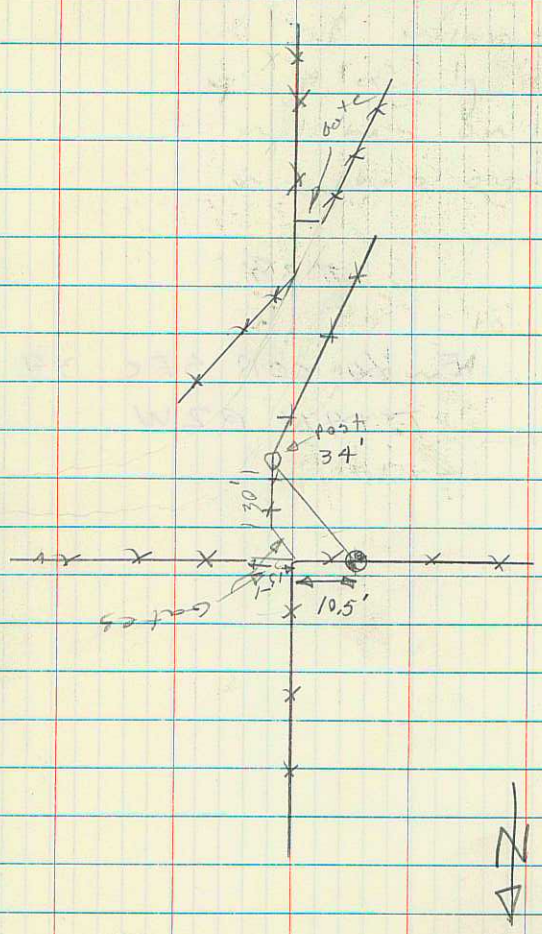
60°
post
34'
30'
15'
10.5'
N

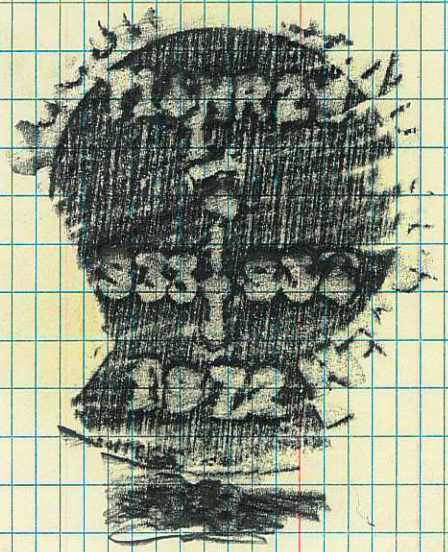

Found a Sandstone
20x12x6 ins firmly set
and very plainly marked
1/4 on E. face.

Set 2" I.P. 24" long
18" in the ground.
Bury orig. Cor. Stone
alongside I.P.

JB

87

7-7-72

#39

SE COR SEC 32

T14N R2W

L-11-9-72

Found a Sandstone 16x12x6 ins. firmly set in mound of stone and very plainly marked with 4 notches on E. and 2 notches on W. edges.

Set 2' I.P. 24" long 18 ins. in ground bury orig. cor. along side I.P. collar of stone around I.P. (No concrete)

This corner is at the head of a small draw which drains S 45° E. in dense oak brush.

Western Union Radio tower bears S 46° E.



7-13-72 BS


#40

NE COR SEC 9
T14N R2W

11-9-72

Found a limestone 18x11x7 ins. firmly set and very plainly marked with 3 notches on E. and 5 notches on S. faces.

Set 2" I.P. 24" long 18" in ground with orig. stone alongside I.P.

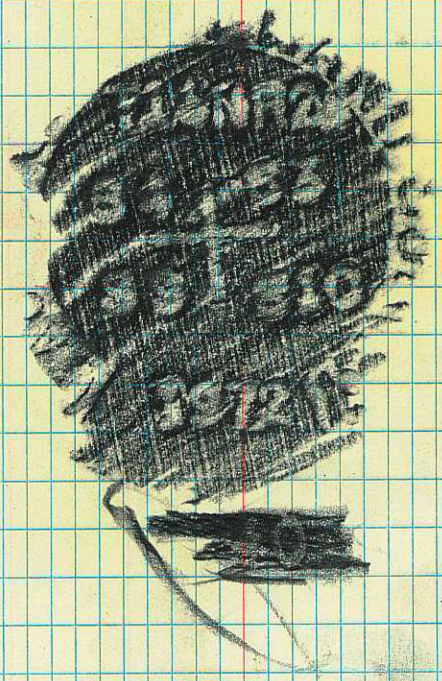

9½

7-14-72

#41

NE COR SEC 12


T14N R1E

~ 11-9-72

Set 2" I.P. 24" long 18" in ground.

Raise mound of stone north of cor.

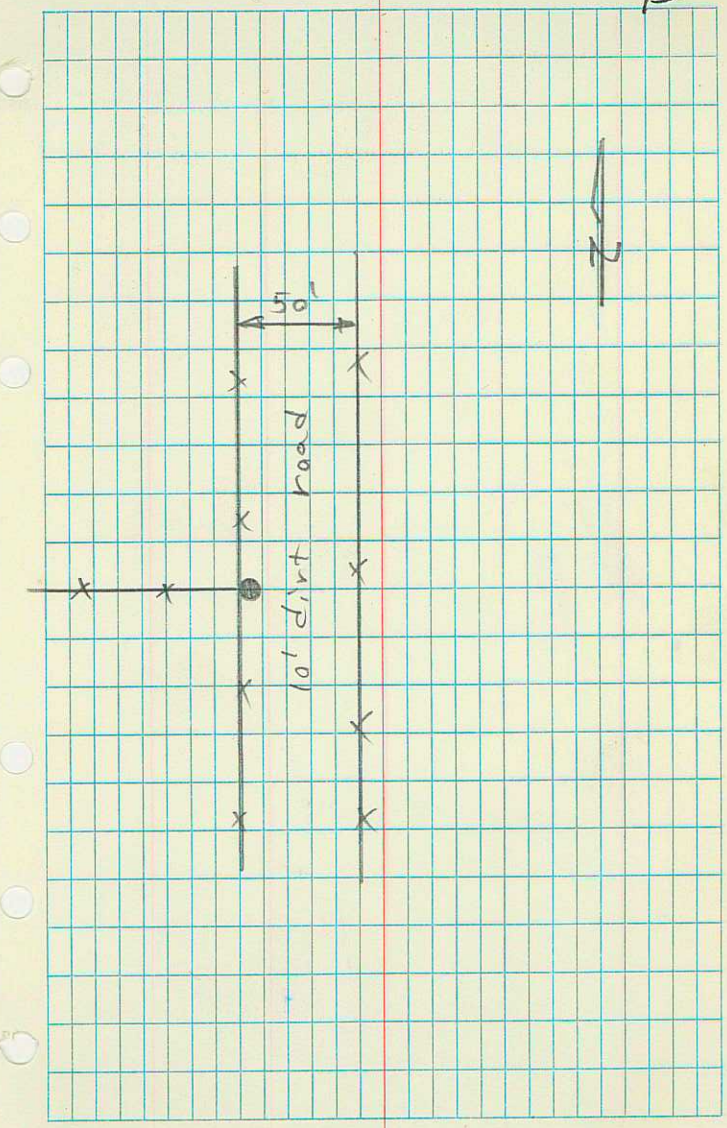


50'
10' dirt road

7-14-72 94

#12


N 1/4 COR SEC 12

T14N R1E

11-9-72

set 2" I.P. 24' long
18" in ground

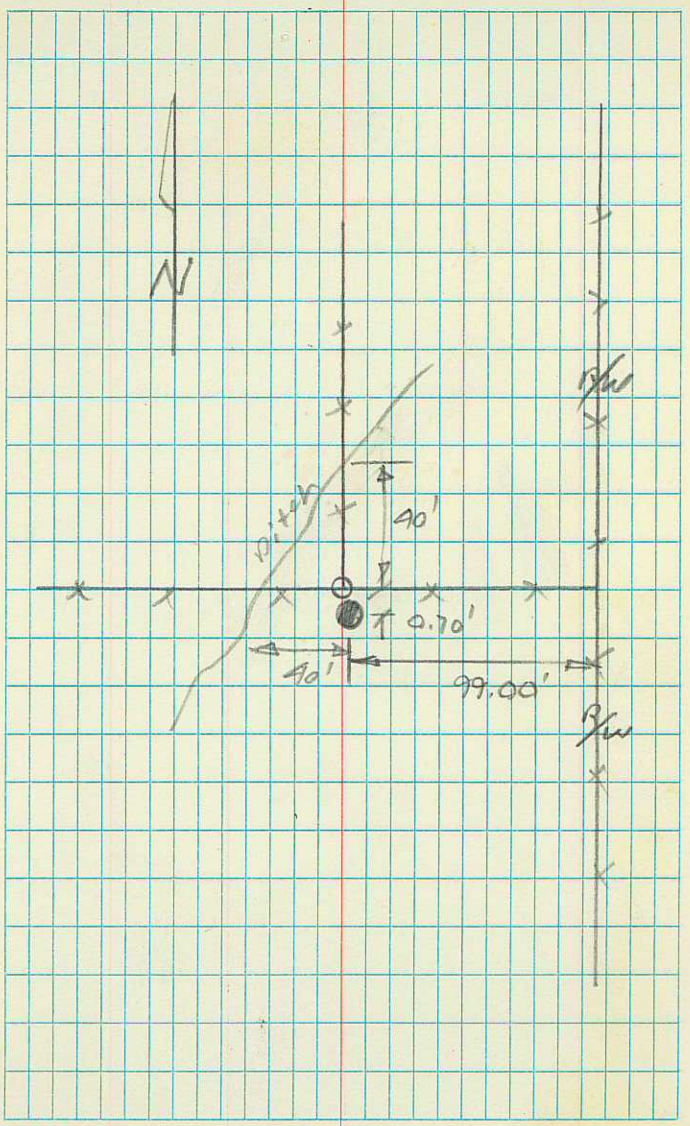


N
R/W
40'
0.70'
40'
99.00'
R/W

7-19-92


#43

N ¼ COR SEC 22

T 14 N R 2 W


Found a Sandstone ~~Timest~~
17 x 12 - 6 ins. firmly
set and very plainly
marked 1/4 on W. face

Set 2" I.P. 24" long
18" in the ground. Bury
orig. cor. alongside
I.P.

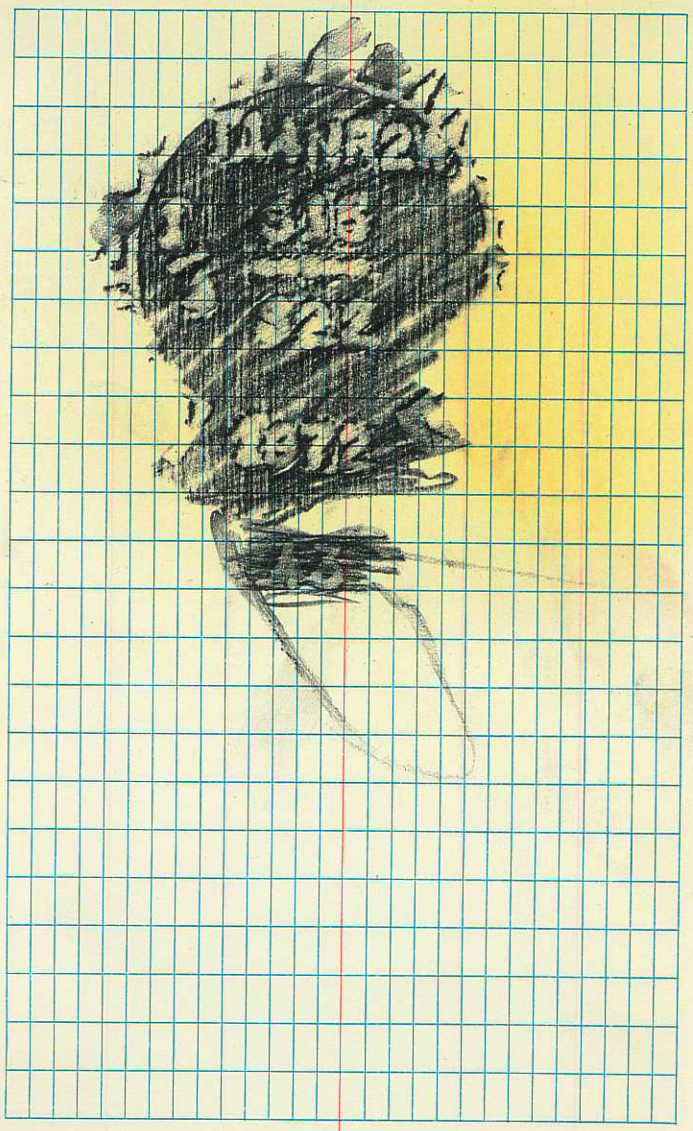

#43

99

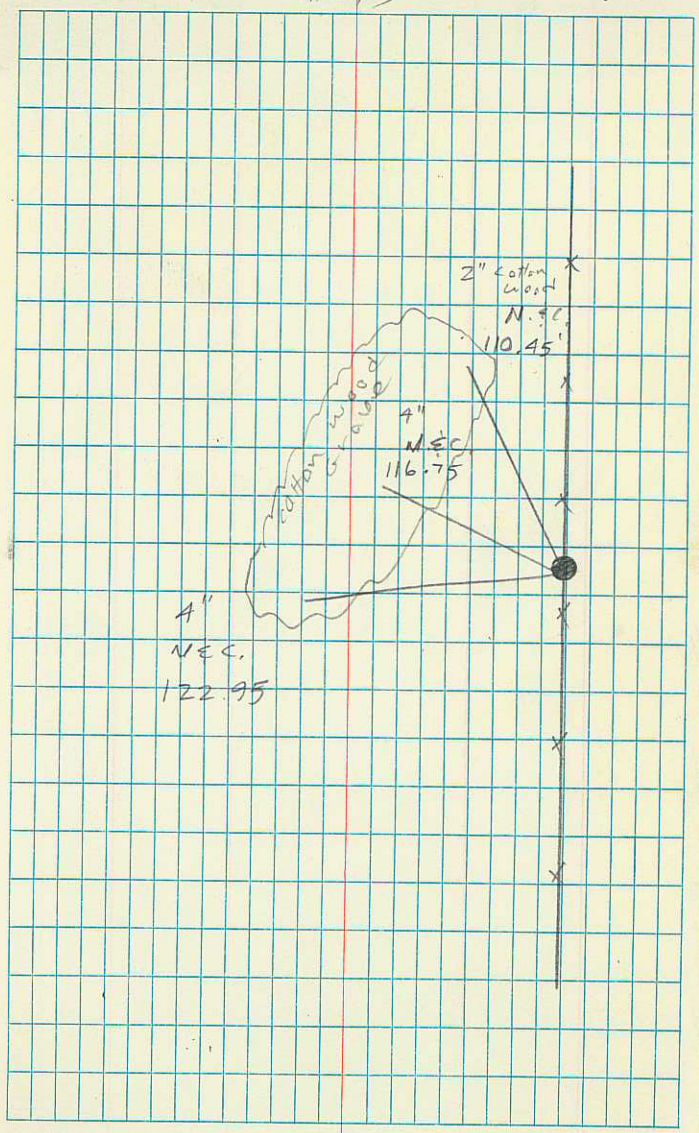

100

7-19-72

#44


E. 1/4 COR SEC. 7


T14N R2W

~ 11-9-72

Found a limestone 12x12x4 ins. firmly set and very plainly mkd. ¼ on E face

Set 2" I.P. 24" long 18" in ground. Bury original Stone alongside I.P.

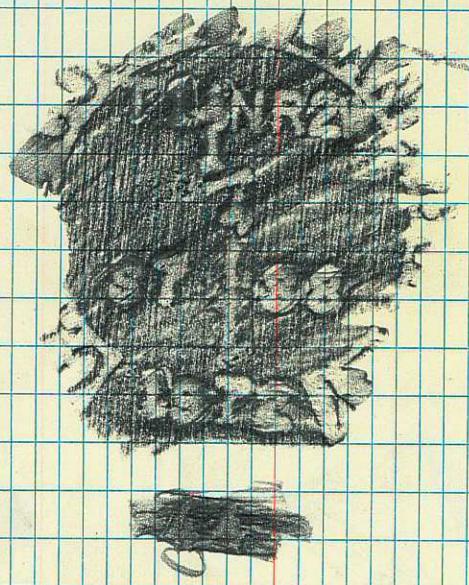

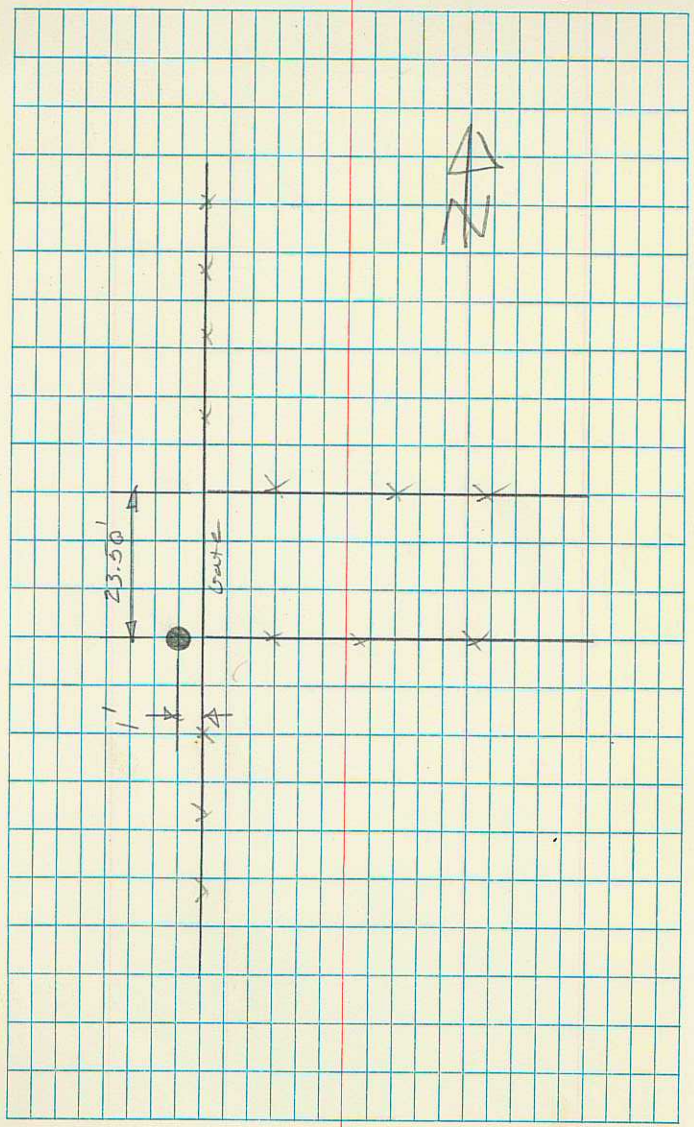
N
23.50'
Center

103

7-19-72

#415


N 1/4 COR SEC 16


T 14N R 2W

11-9-72

Found a limestone 15 x 9 x 7 ins lying loose on ground at fence corner very plainly mkd 1/4 on one face.

Set 2" I.P. 24" long 18" in the ground bury original stone alongside I.P.

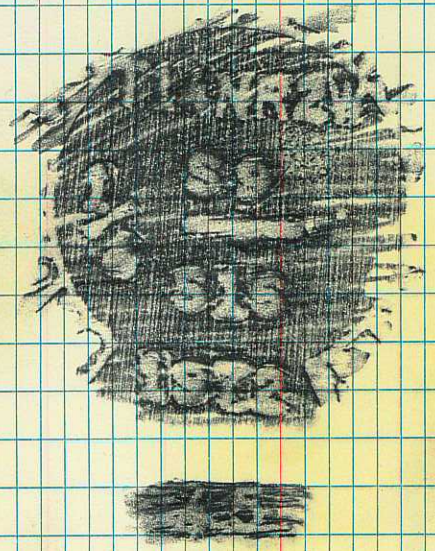

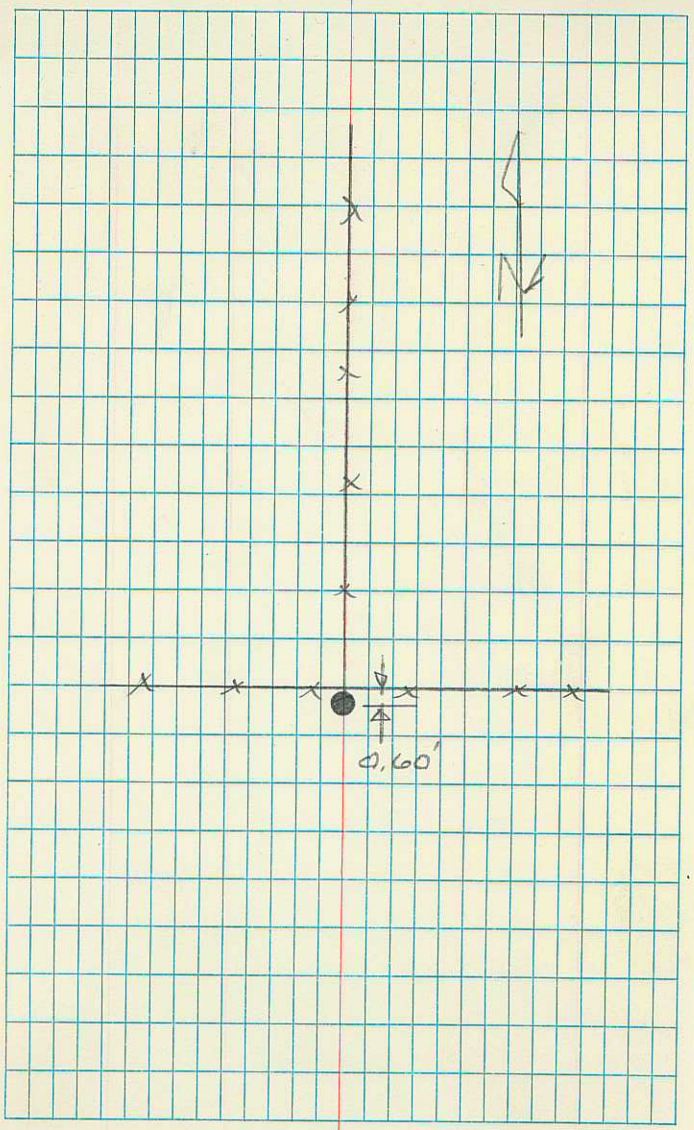
0,60'

106

7-20-72

46

N 1/4 COR SEC. 4

T 13N R 2W


11-9-72

Found a conglomerate stone 18 x 12 x 4 ins. firmly set and very plainly mkd ¼ on N. face.

Set 2" I.P. 24" long 18" in ground. Bury orig. stone alongside I.P.

Raise a mound of stone N. of cor.

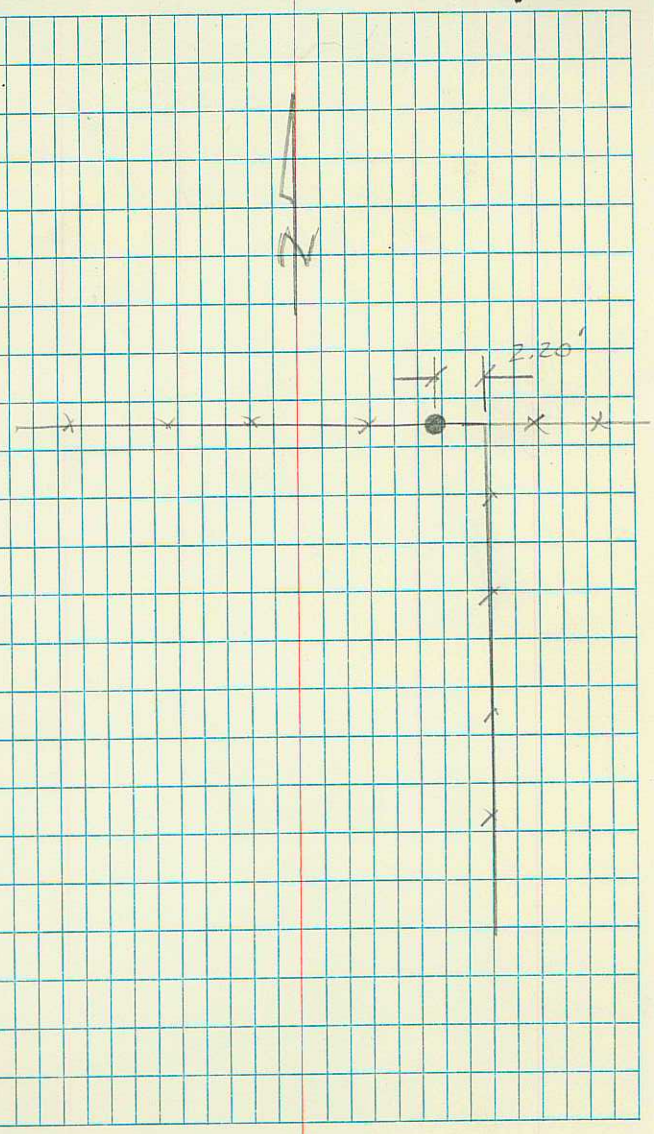


N
2.20'

109

7-20-72

#47

E1/4 Cor SEC 28


T14N R2W

11-9-72

Found a sandstone 17x14x5 ins. lying loose on ground at fence corner very plainly marked 1/4 on one face.

Set 2" I.P. 24" long 18" in ground at fence corner. Bury original stone alongside I.P.

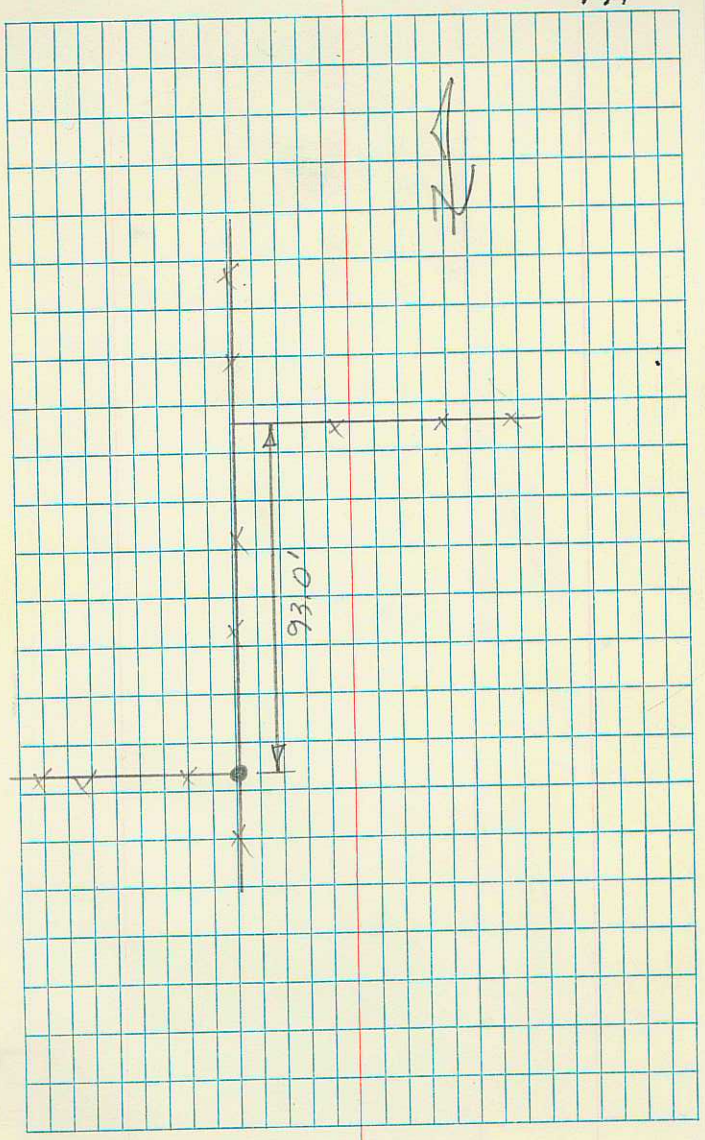


93.0'


112

7-28-72

#48

Found a quartzite stone 2 4x9x9 ins. firmly set and very plainly mkd. with 3 notches on E & W. faces and a possible "c" mkd. on W. face.

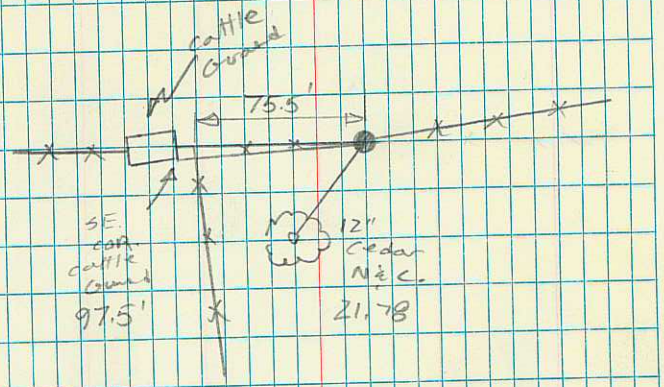


Cattle Guard
75.5'
S.E. cor. cattle Guard
97.5'
12" Cedar N. & C.
21.78

115

7-31-72

#49


E 1/4 COR. SEC. 11


T14N R2W

Found a limestone 13 x 13 x 8 ins. firmly set and very plainly mkd. 1/4 on W. face.

Set 2" I.P. 24" long 18" in the ground.

Bury orig. stone along side I.P.

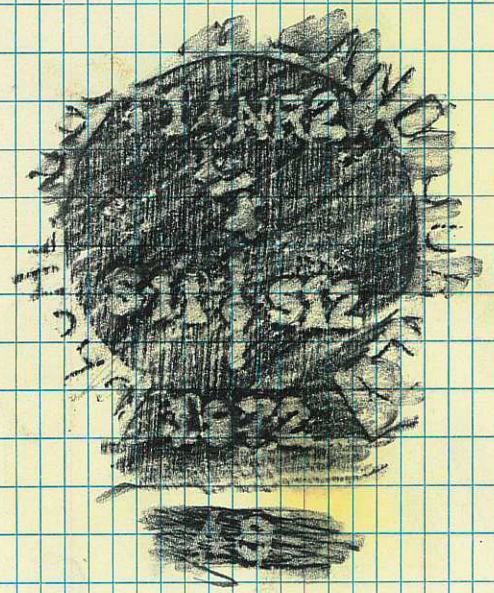

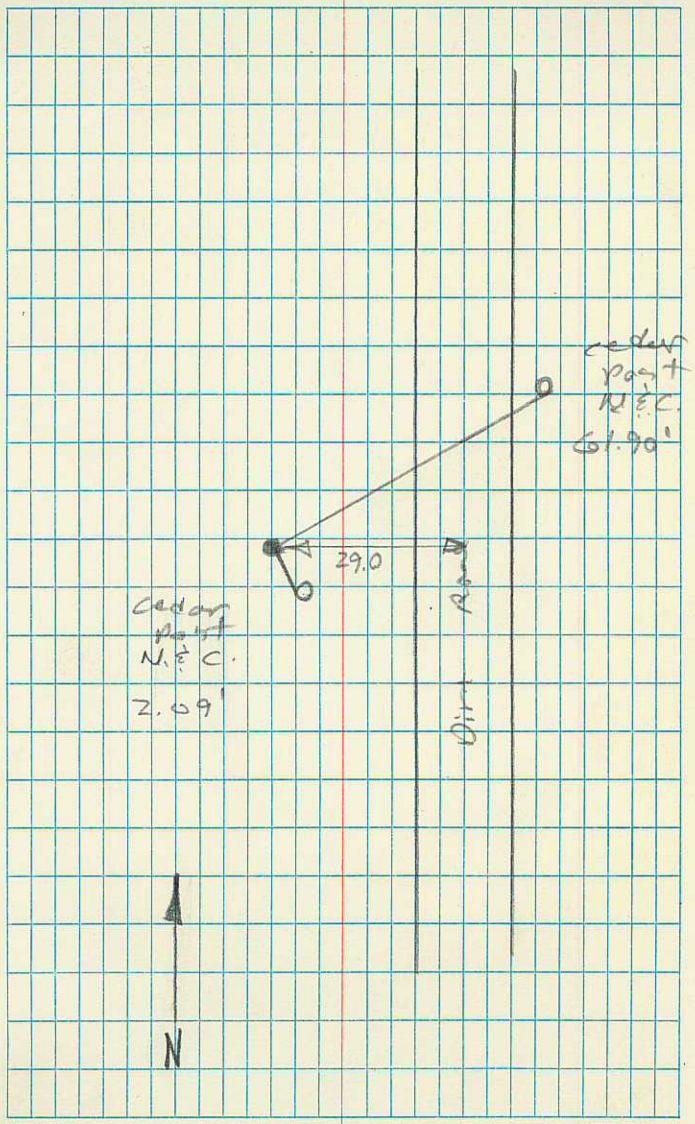
cedar
pt.
N.E.C.
61.90'
29.0
Cedar
Pt.
N.E.C.
2.09'
N

110

7-31-72


#50


NE cor. SEC. 1

T 14 N R 2 W

Found a sandstone 14x12x5 ins. firmly set and very plainly Mkd. with 5 notches on W. and 1 notche on E. faces.

set 2' I.P. 24" lay 18" in gd. with orig. cor. stone ind. sig. side I.P.

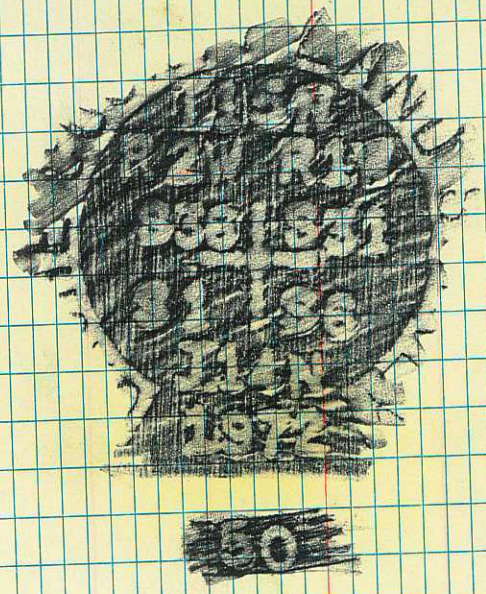

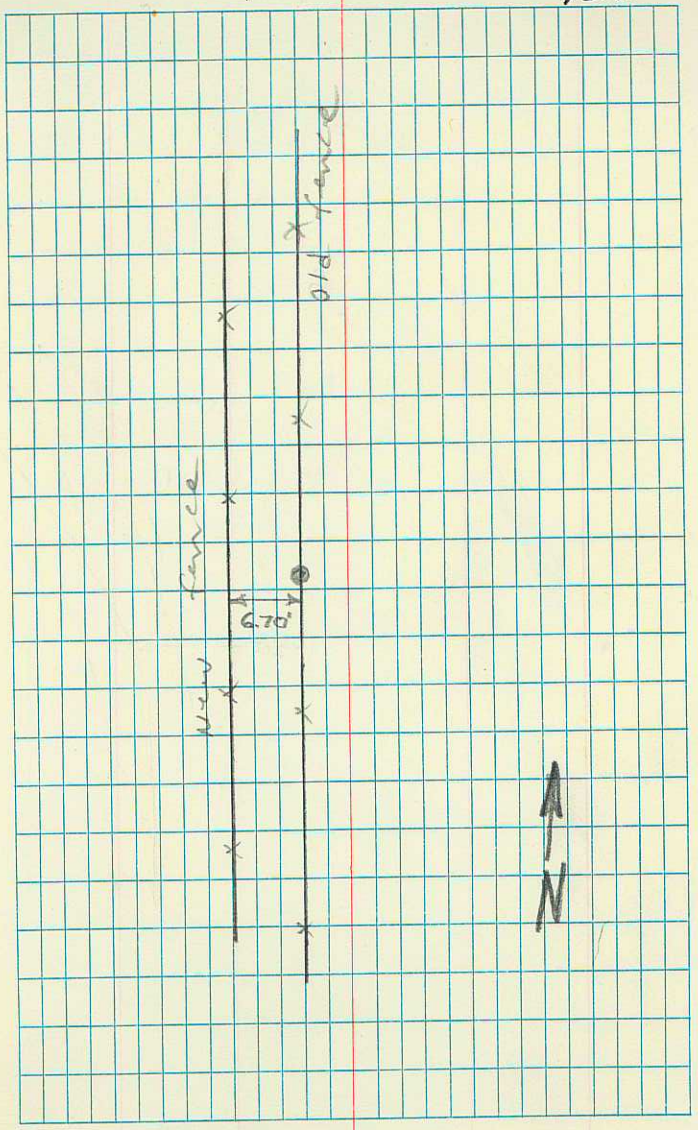
Fence
Old Fence
4.0 ft
N

8-16-12

#51


NE COR SEC 17

T14N R24W

Found a limestone 24x8x8 ins. firmly set and very plainly mkd. with 4 notches on South and East edges.

Set 2" I.P. 24" long 18" in ground. Bury orig. stone alongside I.P. (No concrete)

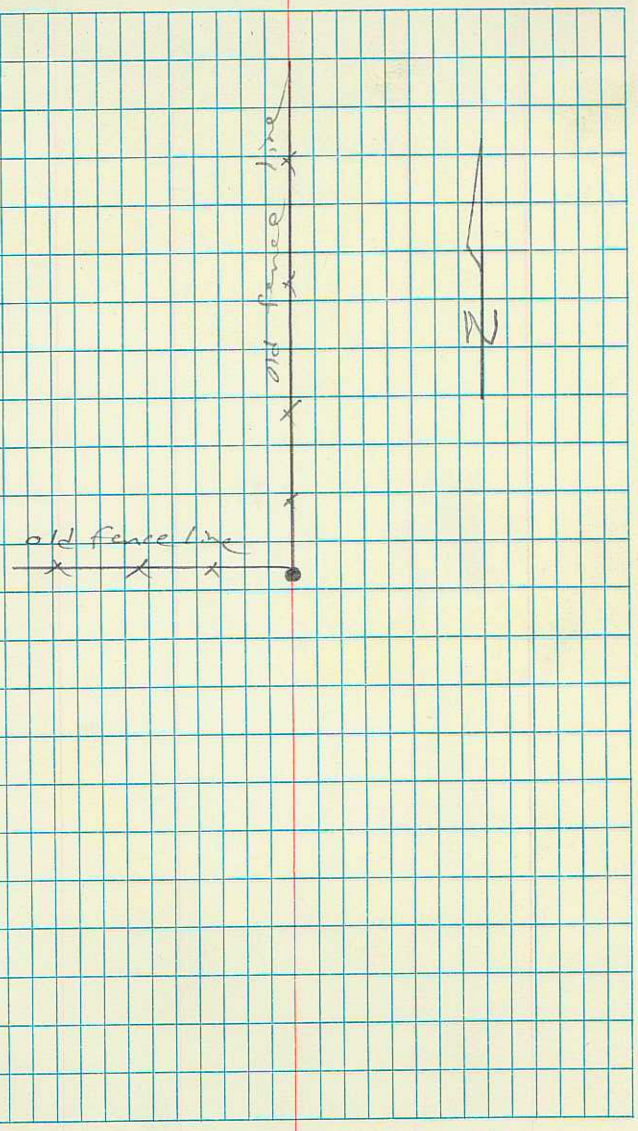


old fence line
old fence line
N

124

8-16-72


#52


NE cor SE 33

T 15 N R 2 W

Found a limestone 14x12x7 ins. firmly set and very plainly mkd. with 3 notches on W. and E. faces and possibly one notch on South edge.

Set 2" I.P. 24" long 18" in ground. Bury orig. cor. alongside I.P. (No concrete)

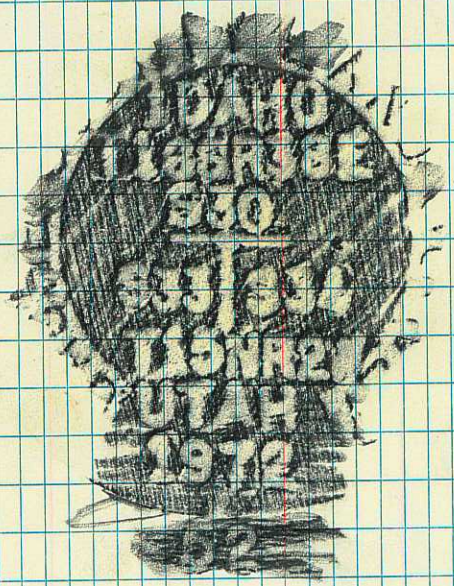

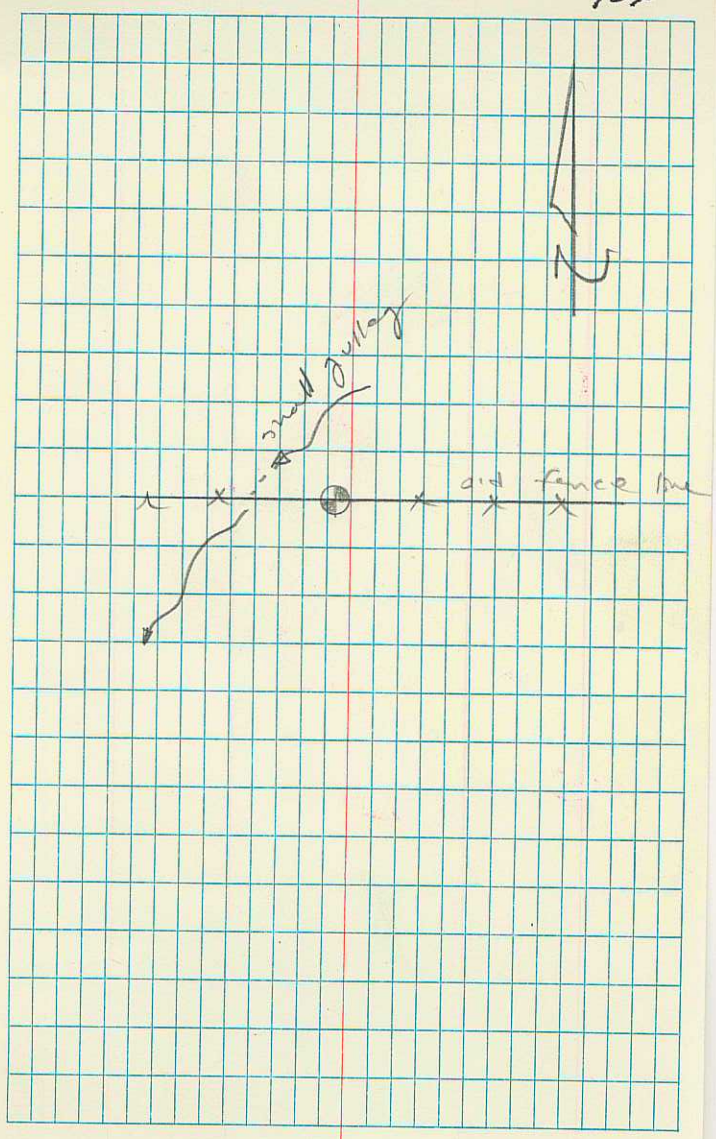
small gully
old fence line


8-24-72


#53

N¼ COR SEC. 4
T10N R1W

Found a sandstone 14 x 9 x 5 in. firmly set and very plainly mkd. 1/4 on N. face.

Set 2" I.P. 18" long 17" in the ground. Bury orig. stone alongside I.P.

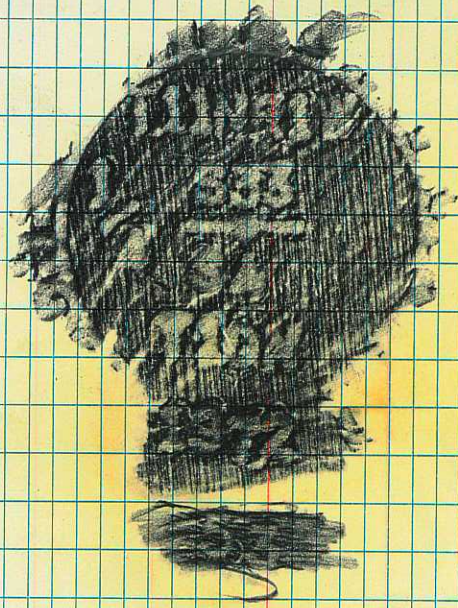

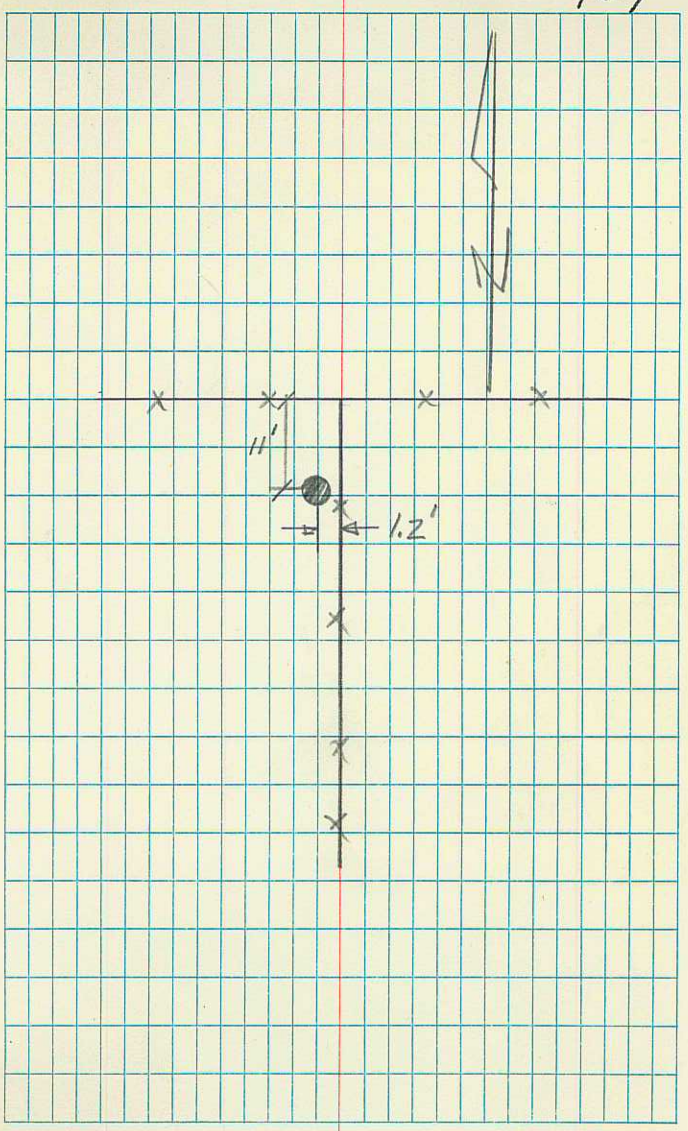
11'
1.2'

130

8-24-72


54


NE COR SEC 4

T10N R1W

Found a Sandstone 15 x 12 x 9 ins. loosely set and very plainly MKd. With 3 notches on E. & W. edges.

Set 2" I.P. 18" long 14" in the ground. Bury orig. Cor. Stone alongside I.P.

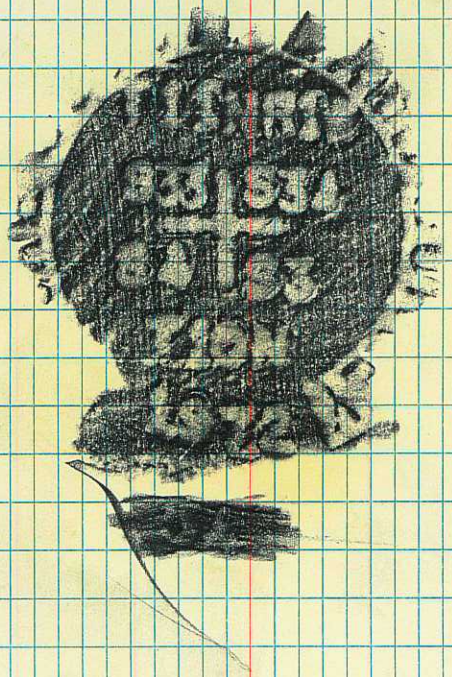

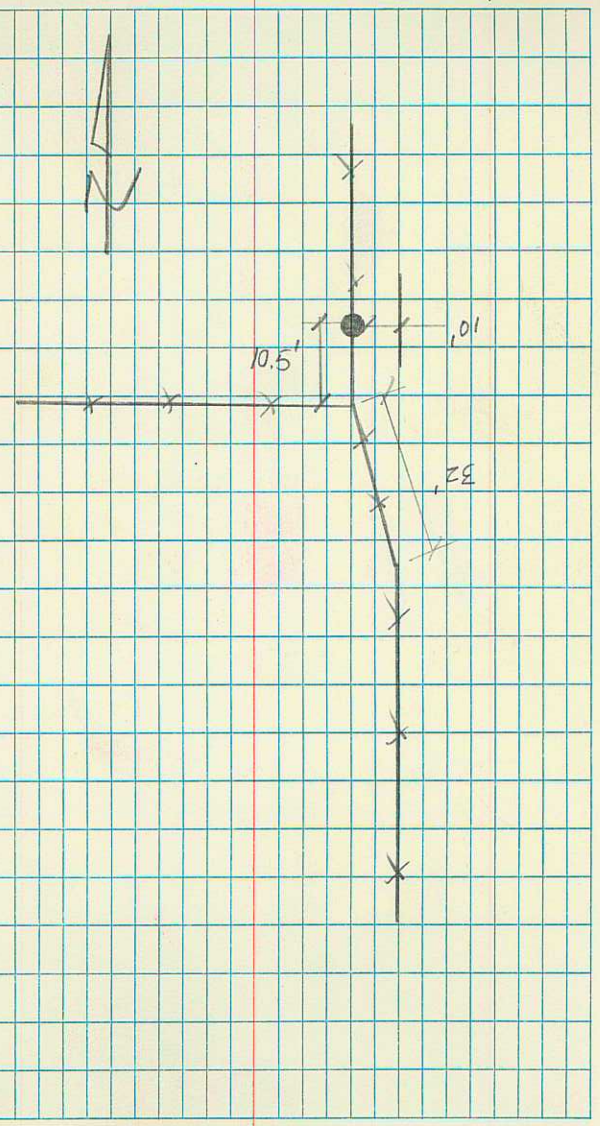
10.5'
.01
32'

133

8-28-72

#55


N 1/4 COR SEC 4

T 13 N R 1 W

Found a Sandstone
16 x 12 x 9 fairly set and
very plainly MKd 1/4 on
South face.

Set 2" I.P. 24" long 18"
in the ground. Bury
orig. Stone alongside I.P.

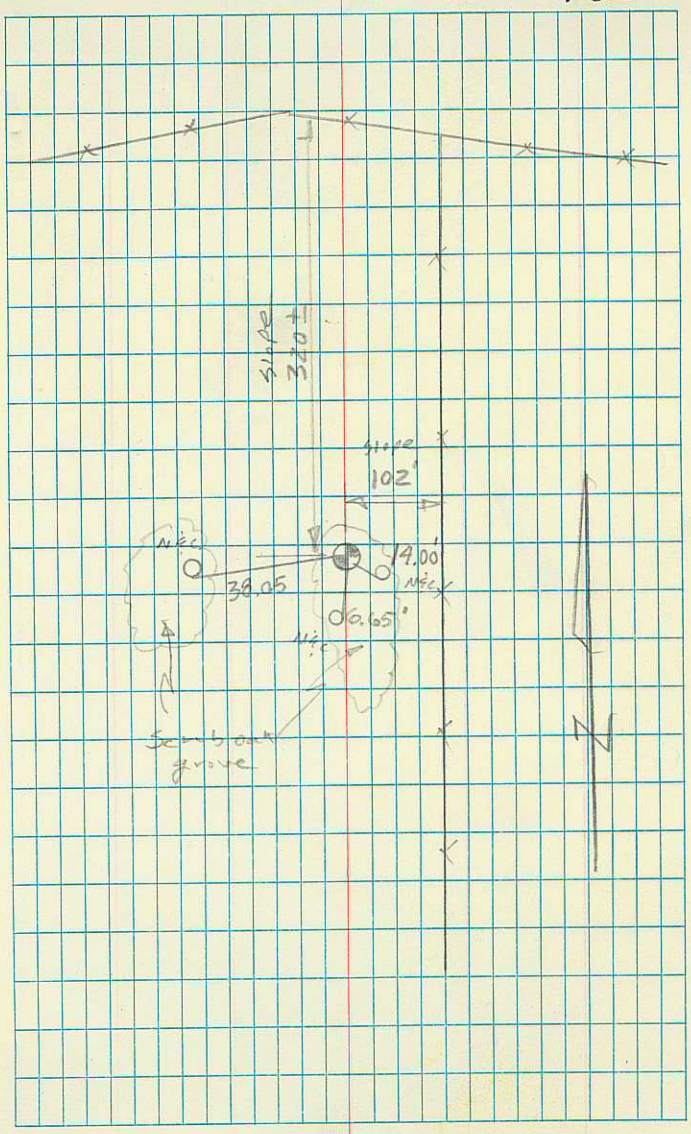


Stone
320'
Stone
102'
N/C
39.05'
19.00'
N/C
060.65°
N/C
Sandbank
Stone

135

8-30-72


#56


NE COR SEC 11

T9N R1E

Found a sandstone 16x9x7 ins. firmly set with no visible markings. Corner was varified by Erwin Moser.

Set 2" I.P. 24" long 18" in the ground Bury any stone cut along side I.P.

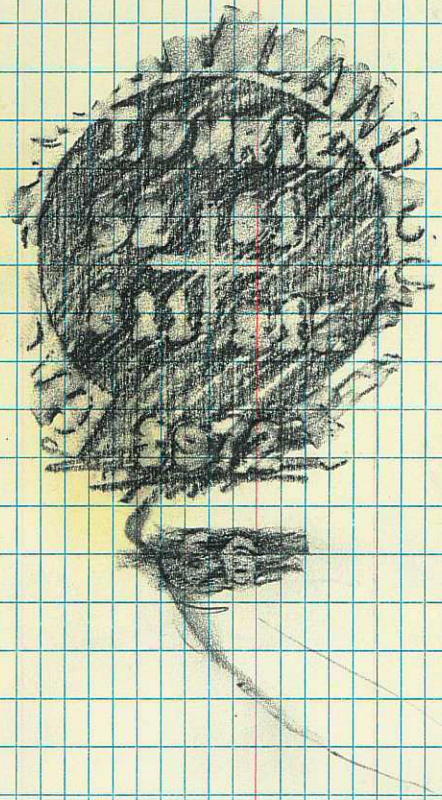

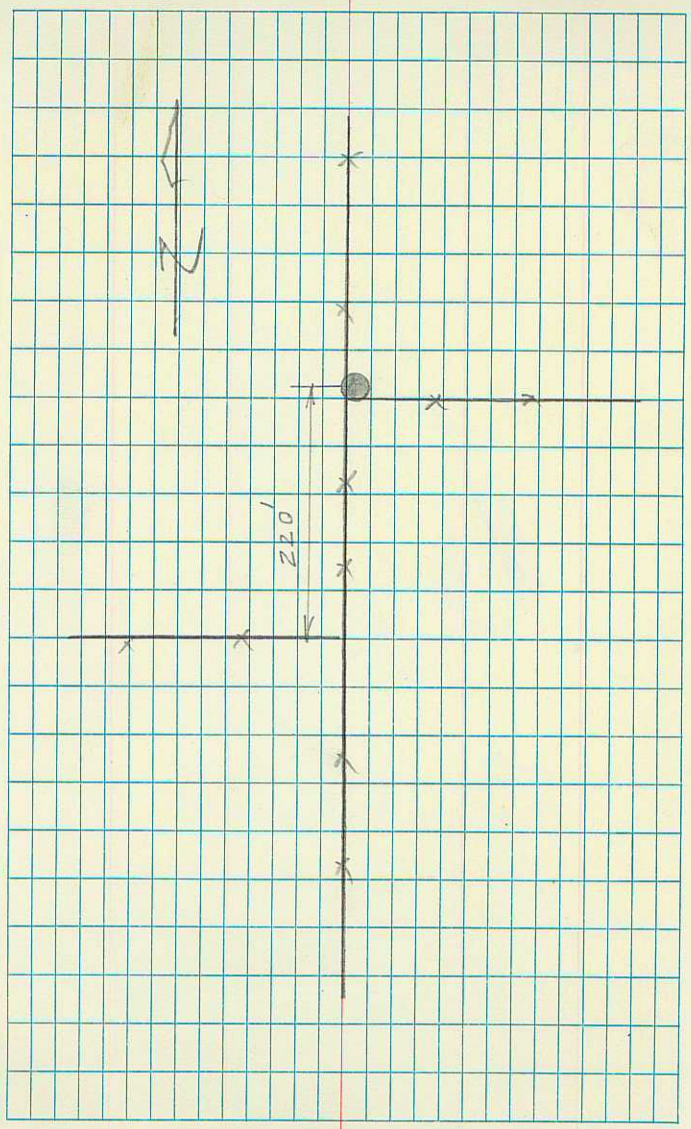
N
012


8-31-72


#57

N 1/4 COR SEC 23
T 13N R 2W

Found a sandstone 22x10x7 ins. firmly set and very plainly mkd. 1/4

Set 2" I.P. 24 long. 18" in the ground Bury orig. stone alongside I.P.

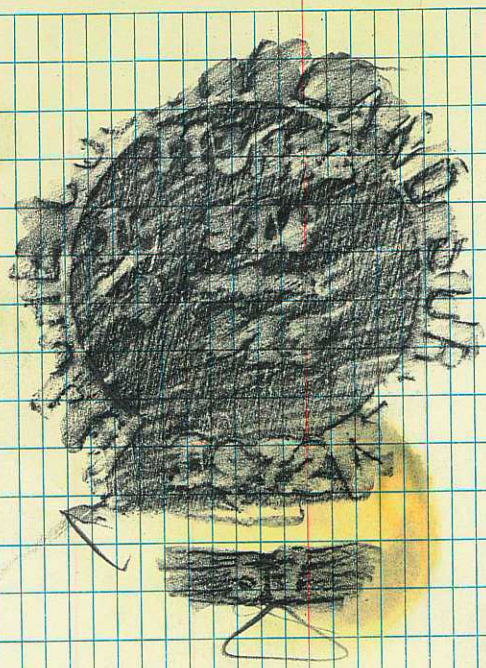

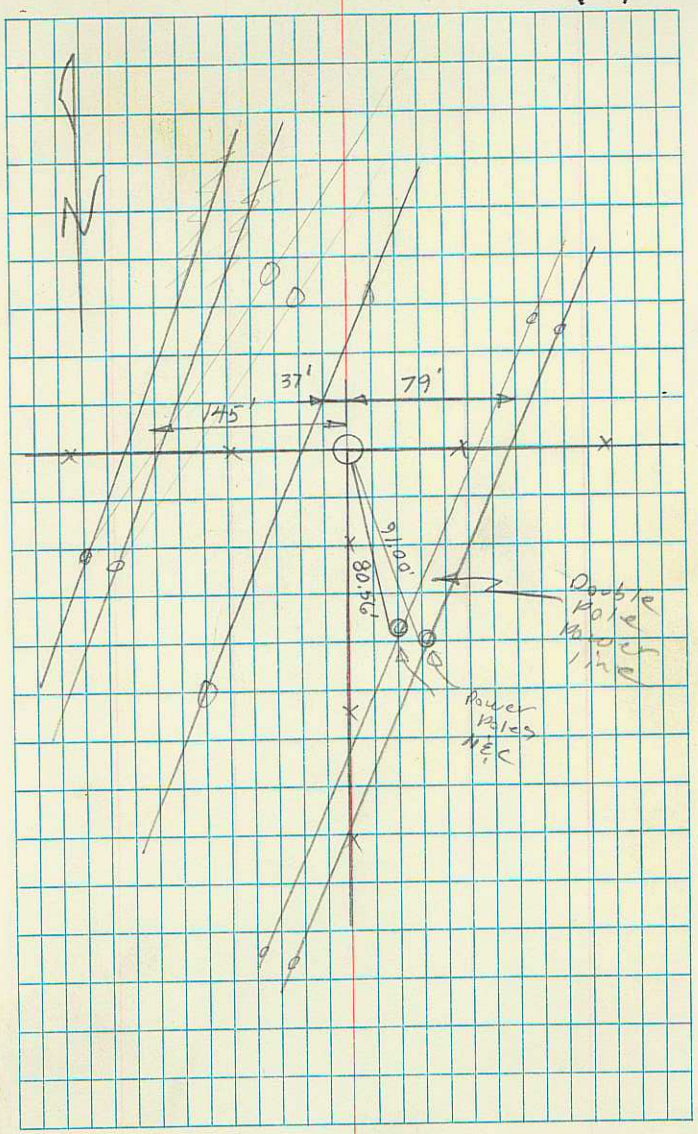
37'
79'
145'
9,100'
80.56'
Double
Power
Power


58


E 1/4 COR. SEC. 35
T 12N R 11E

✓ 11-9-72

No evidence of original cor. stone exact point for corner established by Valley Eng. from breakdown of Sec. 36

Set 2" I.P. 24" long 19" in the ground.

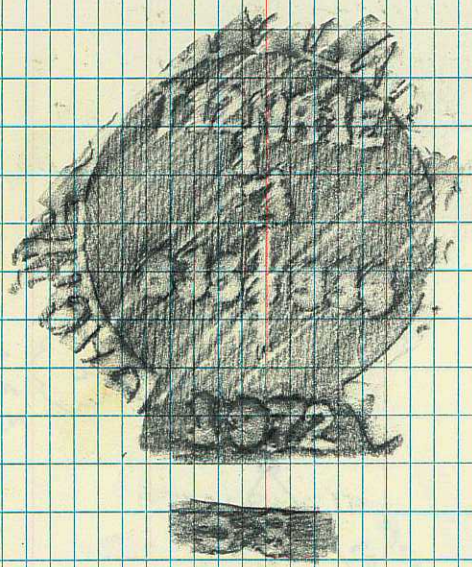

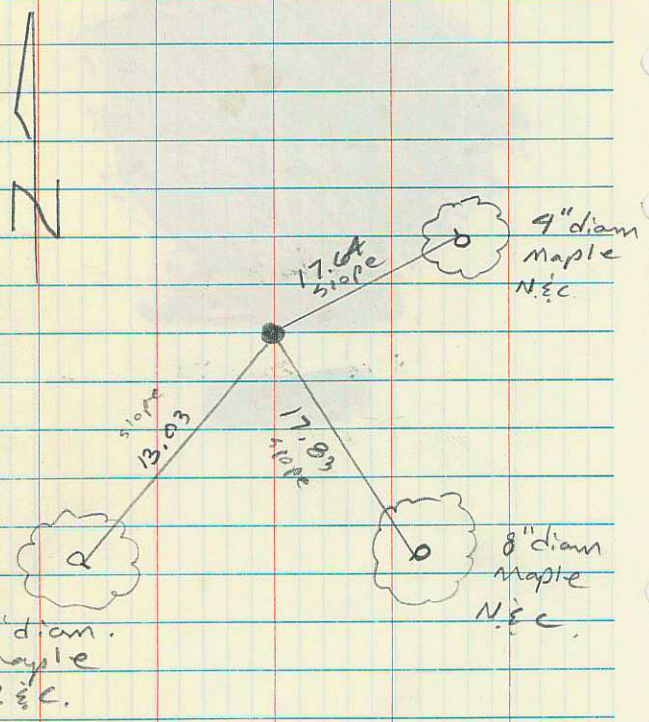

59


N 1/4 of SEC. 36


T11N R1E

11-9-72

No evidence of original corner stone. Exact corner point established by Valley Eng. from breakdown of section 36.

Set 2" I.P. 24" long 7" in the ground with mound of stone 4' base to brass cap

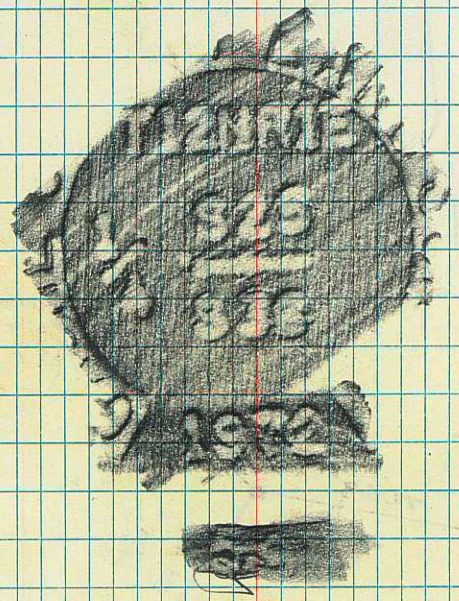

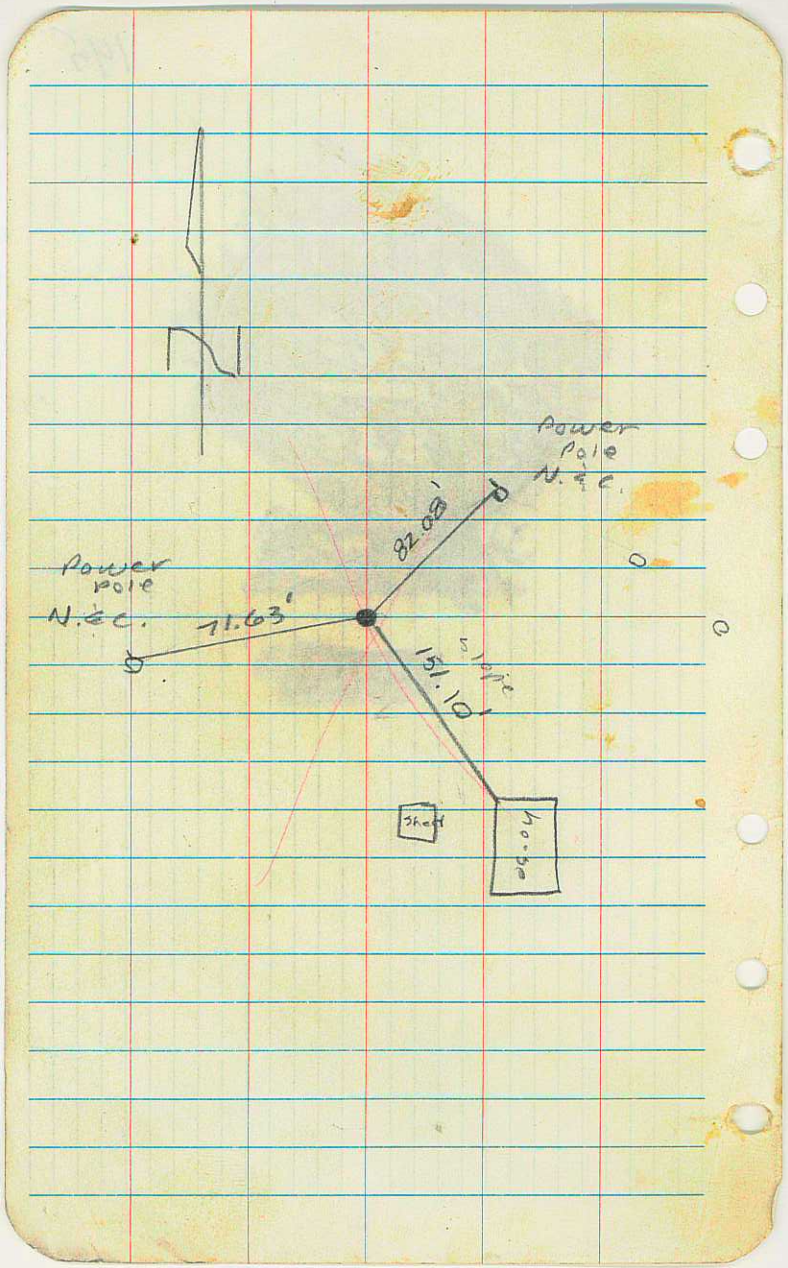
Power Pole N.E.C.
82.09'
Power Pole N.E.C.
71.63'
151.10'
Shed
House
